


S13-500 MOD4 LexEVS Project Plan

ID	JIRA#	% Complete	Task Name	Duration	Predecessor	Start	Finish
0		13%	S13-500 MOD4 LexEVS Project Plan	247.13 days		Wed 10/1/14	Fri 9/18/15
1		100%	Initiate	7.13 days		Wed 10/1/14	Fri 10/10/14
2		100%	Contract Sign-off	0 days		Wed 10/1/14	Wed 10/1/14
3		100%	Project Kick-off	1 hr	2FS+7 days	Fri 10/10/14	Fri 10/10/14
4		13%	Planning & Control	241.13 days		Wed 10/1/14	Thu 9/10/15
5		13%	Project Management	241.13 days		Wed 10/1/14	Thu 9/10/15
6		100%	Update Project Wiki	21 days	2	Wed 10/1/14	Wed 10/29/14
7		9%	Monthly Status & Financial Reporting	213.13 days		Mon 11/10/14	Thu 9/10/15
8		100%	Monthly Status & Financial Reporting 1	1 hr		Mon 11/10/14	Mon 11/10/14
9		0%	Monthly Status & Financial Reporting 2	1 hr		Wed 12/10/14	Wed 12/10/14
10		0%	Monthly Status & Financial Reporting 3	1 hr		Mon 1/12/15	Mon 1/12/15
11		0%	Monthly Status & Financial Reporting 4	1 hr		Tue 2/10/15	Tue 2/10/15
12		0%	Monthly Status & Financial Reporting 5	1 hr		Tue 3/10/15	Tue 3/10/15
13		0%	Monthly Status & Financial Reporting 6	1 hr		Fri 4/10/15	Fri 4/10/15
14		0%	Monthly Status & Financial Reporting 7	1 hr		Mon 5/11/15	Mon 5/11/15
15		0%	Monthly Status & Financial Reporting 8	1 hr		Wed 6/10/15	Wed 6/10/15
16		0%	Monthly Status & Financial Reporting 9	1 hr		Fri 7/10/15	Fri 7/10/15
17		0%	Monthly Status & Financial Reporting 10	1 hr		Mon 8/10/15	Mon 8/10/15
18		0%	Monthly Status & Financial Reporting 11	1 hr		Thu 9/10/15	Thu 9/10/15
19		9%	Ongoing Project Management	12 mons		Wed 10/1/14	Wed 9/9/15
20		9%	Ongoing Project Oversight	12 mons		Wed 10/1/14	Tue 9/8/15
21		14%	Execute	240 days	3	Fri 10/10/14	Fri 9/18/15
22		9%	Ongoing Operational Support	240 days	3	Fri 10/10/14	Fri 9/18/15
23		9%	Tech Support/Forum Management/Ongoing Technical Expertise	12 mons		Fri 10/10/14	Fri 9/18/15
24		0%	Milestone: Ongoing Operational Support Complete	0 days	22	Fri 9/18/15	Fri 9/18/15
25		65%	Maintenance and Support Development	25 days	3	Fri 10/10/14	Fri 11/14/14
26		100%	Supporting Item Development	6 days		Fri 10/10/14	Mon 10/20/14
27		100%	AMIA Poster	1 wk		Fri 10/10/14	Mon 10/20/14
28		100%	Milestone: Supporting Item Development Complete	0 days	26	Mon 10/20/14	Mon 10/20/14
29		59%	JIRA Item Development	25 days	3	Fri 10/10/14	Fri 11/14/14
30	LEXEVS-671	100%	SNOMEDCT does not load hierarchy or root nodes.	1 wk		Fri 10/10/14	Fri 10/17/14
31	LEXEVS-669	100%	Latest Version of SNOMEDCT Does not load transitivity table	2 wks	30	Fri 10/17/14	Fri 10/31/14
32	LEXEVSCTS2-21	50%	Value Set resolution fails when a value set name is more than a particular number of characters.	3 days	27FS+1 wk	Mon 10/27/14	Thu 10/30/14
33	LEXEVS-667	0%	TreeService getTree method fails on remote call when the root node code appears in multiple namespaces.	2 wks	31	Fri 10/31/14	Fri 11/14/14
34		0%	Milestone: JIRA Item Development Complete	0 days	29	Fri 11/14/14	Fri 11/14/14
35		0%	Milestone - Maintenance and Support Development Complete	0 days	25	Fri 11/14/14	Fri 11/14/14
36		0%	Update Technical Documentation	10 days	25	Fri 11/21/14	Mon 12/8/14
37		0%	Project Closure	2 days	25FS+1 wk	Fri 11/21/14	Tue 11/25/14
38		0%	Design and Architecture Guide	2 days	37	Tue 11/25/14	Fri 11/28/14
39		0%	Programmer's Guide	2 days	38	Fri 11/28/14	Tue 12/2/14

S13-500 MOD4 LexEVS Project Plan

ID	JIRA#	% Complete	Task Name	Duration	Predecessor	Start	Finish
40		0%	Install Guide	2 days	39	Tue 12/2/14	Thu 12/4/14
41		0%	Administrator Guide	2 days	40	Thu 12/4/14	Mon 12/8/14
42		0%	Milestone: Update Technical Documentation Complete	0 days	36	Mon 12/8/14	Mon 12/8/14
43		0%	Operational Readiness Review	2.5 days	25FS+1 wk	Fri 11/21/14	Tue 11/25/14
44		0%	Create Operational Readiness Review Package	2 days		Fri 11/21/14	Tue 11/25/14
45		0%	Submit Rediness Review Package to COTR for review.	4 hrs	44	Tue 11/25/14	Tue 11/25/14
46		0%	Milestone: Operational Readiness Review Complete	0 hrs	43	Tue 11/25/14	Tue 11/25/14
47		0%	Tier Deployment at NCI	10.11 days		Fri 11/14/14	Mon 12/1/14
48		0%	Dev Deployment	2 days	25	Fri 11/14/14	Tue 11/18/14
49		0%	Deploy Updated LexEVS 6.3	2 days		Fri 11/14/14	Tue 11/18/14
50		0%	Deploy Updated LexEVS 6.3 CTS2 Service	2 days		Fri 11/14/14	Tue 11/18/14
51		0%	Deploy Updated LexEVS 6.3 URI Resolver Service	2 days		Fri 11/14/14	Tue 11/18/14
52		0%	On Site Deployment	3.11 days	48	Tue 11/18/14	Fri 11/21/14
53		0%	QA Deployment	1.11 days	48	Tue 11/18/14	Wed 11/19/14
54		0%	Stage Deployment	2 days	53	Wed 11/19/14	Fri 11/21/14
55		0%	Production Deployment	1 wk	52	Fri 11/21/14	Mon 12/1/14
56		0%	Product Communication	1 day		Fri 11/21/14	Mon 11/24/14
57		0%	Release Notes	2 hrs	52	Fri 11/21/14	Fri 11/21/14
58		0%	Announcement	1 day	52	Fri 11/21/14	Mon 11/24/14
59		0%	Milestone: Tier Deployment at NCI	0 days	47	Mon 12/1/14	Mon 12/1/14
60		0%	Close	0.8 days	52	Fri 11/21/14	Mon 11/24/14
61		0%	Lessons Learned	4 hrs		Fri 11/21/14	Fri 11/21/14
62		0%	Deliverable: Project Summary	0.3 days	61	Fri 11/21/14	Mon 11/24/14
63		0%	Milestone: S13-500 MOD4 LexEVS Project Plan Complete	0 days	47	Mon 12/1/14	Mon 12/1/14

S13-500 MOD4 LexEVS Project Plan

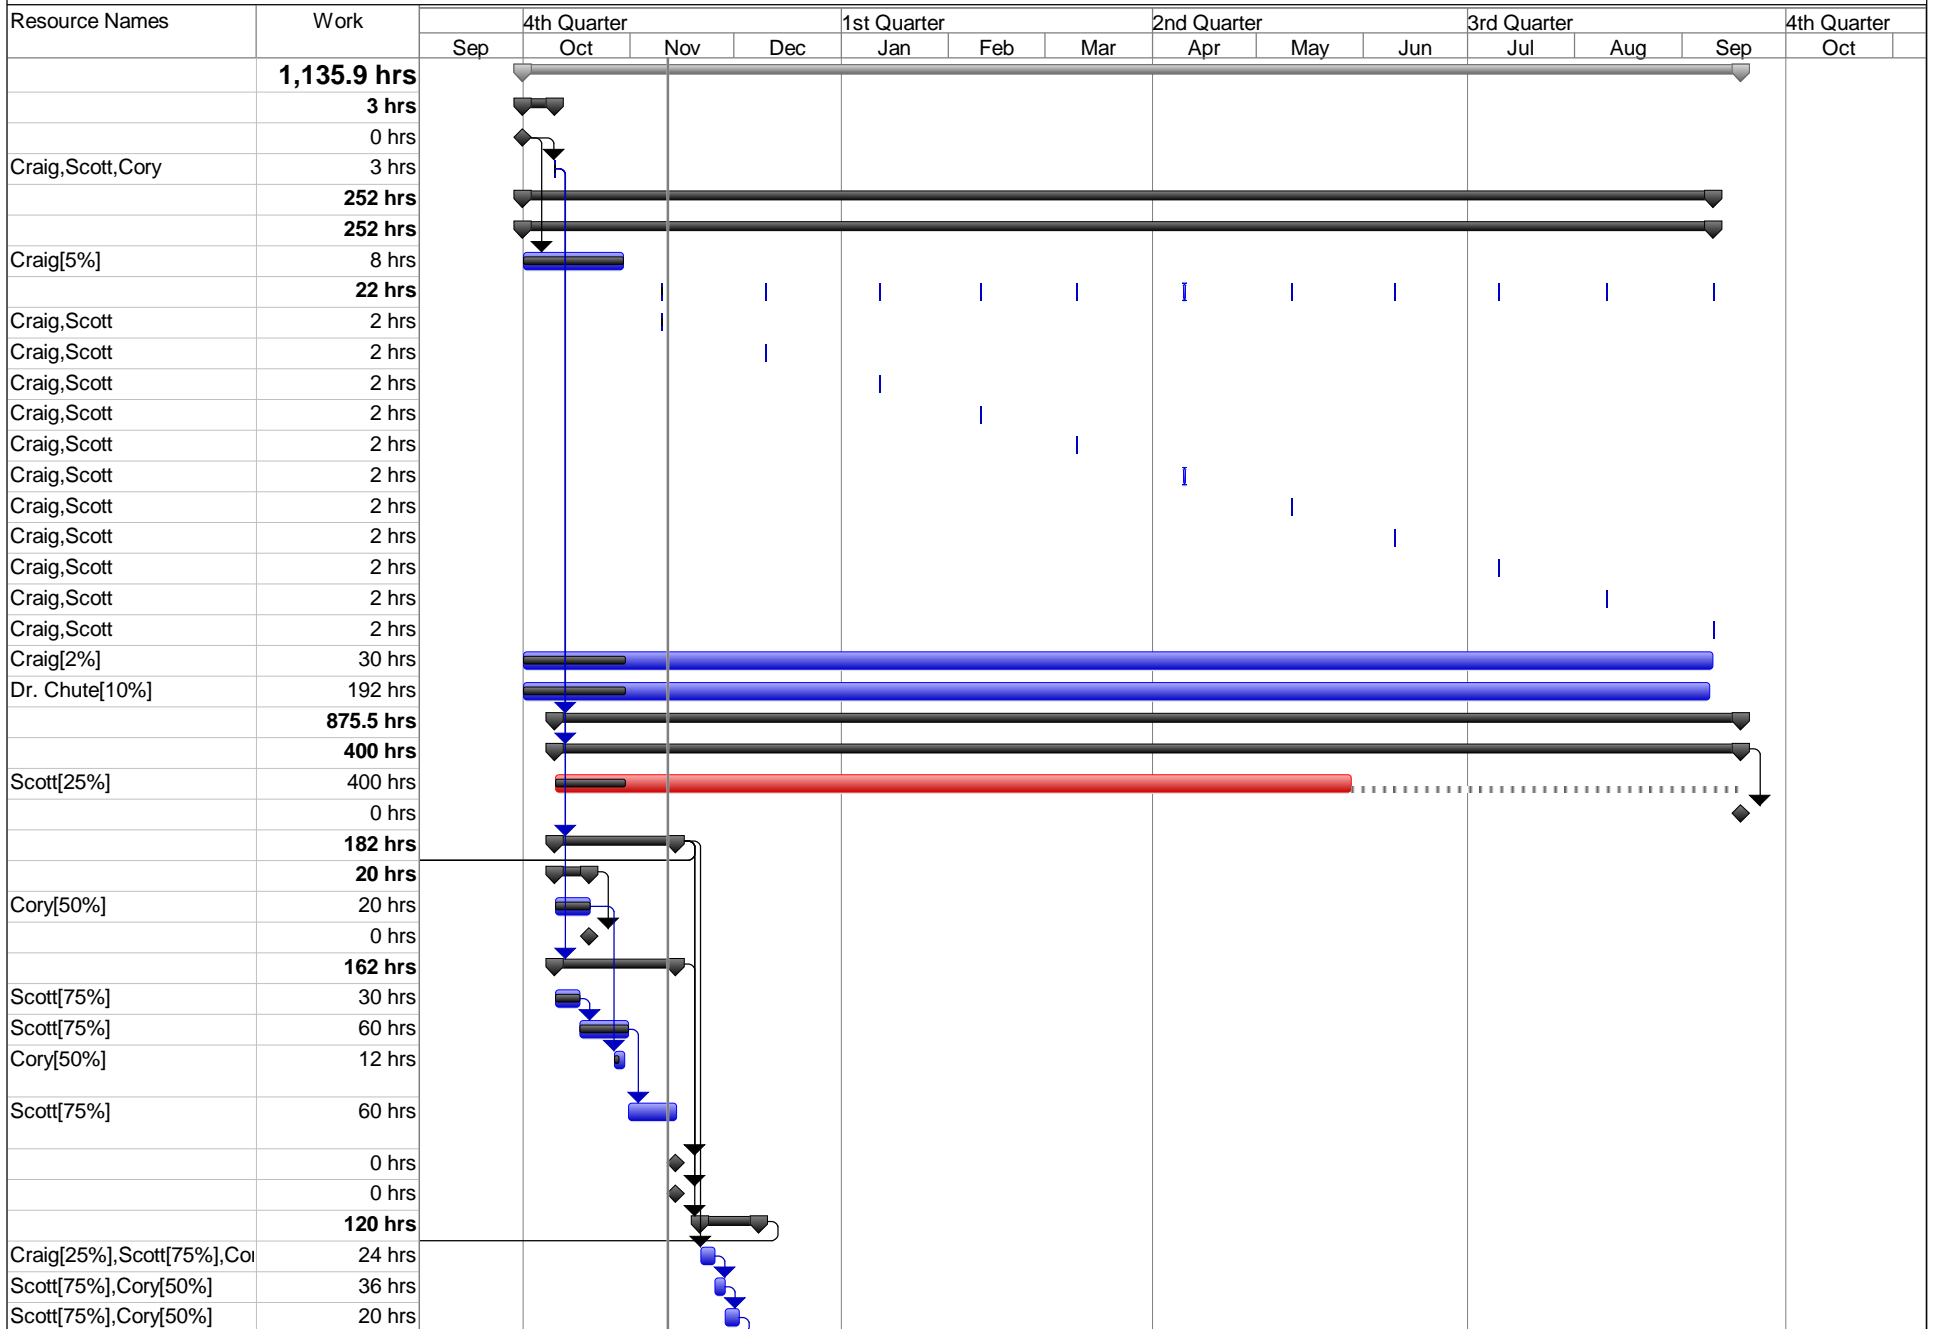

S13-500 MOD4 LexEVS Project Plan

Resource Names	Work	4th Quarter				1st Quarter			2nd Quarter			3rd Quarter			4th Quarter	
		Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	
Scott[75%],Cory[50%]	20 hrs															
Scott[75%],Cory[50%]	20 hrs															
	0 hrs															
	5 hrs															
Craig[25%]	4 hrs															
Craig[25%]	1 hr															
	0 hrs															
	168.5 hrs															
	60 hrs															
Scott[75%],Cory[50%]	20 hrs															
Scott[75%],Cory[50%]	20 hrs															
Scott[75%],Cory[50%]	20 hrs															
	56 hrs															
Scott[75%],Cory[50%],NCI	20 hrs															
Scott[75%],Cory[50%],NCI	36 hrs															
NCI Resource	40 hrs															
	12.5 hrs															
Scott[75%],Cory[50%]	2.5 hrs															
Scott[75%],Cory[50%]	10 hrs															
	0 hrs															
	5.4 hrs															
Craig[25%],Scott[75%],Cory[50%]	3 hrs															
	2.4 hrs															
	0 hrs															
