


S13-500 MOD4 LexEVS Project Plan

ID	JIRA#	% Complete	Task Name	Duration	Predecessors	Start	Finish	Resource Names	Work	Sep
0		16%	<b>S13-500 MOD4 LexEVS Project Plan</b>	<b>247.13 days</b>		<b>Wed 10/1/14</b>	<b>Fri 9/18/15</b>		<b>1,279.15 hrs</b>	
1		100%	<b>Initiate</b>	<b>7.13 days</b>		<b>Wed 10/1/14</b>	<b>Fri 10/10/14</b>		<b>3 hrs</b>	
2		100%	Contract Sign-off	0 days		Wed 10/1/14	Wed 10/1/14		0 hrs	
3		100%	Project Kick-off	1 hr	2FS+7 days	Fri 10/10/14	Fri 10/10/14	Craig,Scott,Cory	3 hrs	
4		13%	<b>Planning &amp; Control</b>	<b>243 days</b>		<b>Wed 10/1/14</b>	<b>Fri 9/11/15</b>		<b>252 hrs</b>	
5		13%	<b>Project Management</b>	<b>243 days</b>		<b>Wed 10/1/14</b>	<b>Fri 9/11/15</b>		<b>252 hrs</b>	
6		100%	Update Project Wiki	21 days	2	Wed 10/1/14	Wed 10/29/14	Craig[5%]	8 hrs	
7		9%	<b>Monthly Status &amp; Financial Reporting</b>	<b>213.13 days</b>		<b>Mon 11/10/14</b>	<b>Thu 9/10/15</b>		<b>22 hrs</b>	
8		100%	Monthly Status & Financial Reporting 1	1 hr		Mon 11/10/14	Mon 11/10/14	Craig,Scott	2 hrs	
9		0%	Monthly Status & Financial Reporting 2	1 hr		Wed 12/10/14	Wed 12/10/14	Craig,Scott	2 hrs	
10		0%	Monthly Status & Financial Reporting 3	1 hr		Mon 1/12/15	Mon 1/12/15	Craig,Scott	2 hrs	
11		0%	Monthly Status & Financial Reporting 4	1 hr		Tue 2/10/15	Tue 2/10/15	Craig,Scott	2 hrs	
12		0%	Monthly Status & Financial Reporting 5	1 hr		Tue 3/10/15	Tue 3/10/15	Craig,Scott	2 hrs	
13		0%	Monthly Status & Financial Reporting 6	1 hr		Fri 4/10/15	Fri 4/10/15	Craig,Scott	2 hrs	
14		0%	Monthly Status & Financial Reporting 7	1 hr		Mon 5/11/15	Mon 5/11/15	Craig,Scott	2 hrs	
15		0%	Monthly Status & Financial Reporting 8	1 hr		Wed 6/10/15	Wed 6/10/15	Craig,Scott	2 hrs	
16		0%	Monthly Status & Financial Reporting 9	1 hr		Fri 7/10/15	Fri 7/10/15	Craig,Scott	2 hrs	
17		0%	Monthly Status & Financial Reporting 10	1 hr		Mon 8/10/15	Mon 8/10/15	Craig,Scott	2 hrs	
18		0%	Monthly Status & Financial Reporting 11	1 hr		Thu 9/10/15	Thu 9/10/15	Craig,Scott	2 hrs	
19		9%	Ongoing Project Management	12 mons		Wed 10/1/14	Fri 9/11/15	Craig[2%]	30 hrs	
20		9%	Ongoing Project Oversight	12 mons		Wed 10/1/14	Tue 9/8/15	Dr. Chute[10%]	192 hrs	
21		21%	<b>Execute</b>	<b>240 days</b>	<b>3</b>	<b>Fri 10/10/14</b>	<b>Fri 9/18/15</b>		<b>1,018.75 hrs</b>	
22		9%	<b>Ongoing Operational Support</b>	<b>240 days</b>	<b>3</b>	<b>Fri 10/10/14</b>	<b>Fri 9/18/15</b>		<b>400 hrs</b>	
23		9%	Tech Support/Forum Management/Ongoing Technical Expertise	12 mons		Fri 10/10/14	Fri 9/18/15	Scott[25%]	400 hrs	
24		0%	Milestone: Ongoing Operational Support Complete	0 days	22	Fri 9/18/15	Fri 9/18/15		0 hrs	
25		82%	<b>Maintenance and Support Development</b>	<b>46.5 days</b>	<b>3</b>	<b>Fri 10/10/14</b>	<b>Tue 12/16/14</b>		<b>325.25 hrs</b>	
26		100%	<b>Supporting Item Development</b>	<b>6 days</b>	<b>3</b>	<b>Fri 10/10/14</b>	<b>Mon 10/20/14</b>		<b>20 hrs</b>	
27		100%	AMIA Poster	1 wk		Fri 10/10/14	Mon 10/20/14	Cory[50%]	20 hrs	
28		100%	Milestone: Supporting Item Development Complete	0 days	26	Mon 10/20/14	Mon 10/20/14		0 hrs	
29		80%	<b>JIRA Item Development</b>	<b>46.5 days</b>	<b>3</b>	<b>Fri 10/10/14</b>	<b>Tue 12/16/14</b>		<b>305.25 hrs</b>	
30	LEXEVS-671	100%	SNOMEDCT does not load hierarchy or root nodes.	1 wk		Fri 10/10/14	Fri 10/17/14	Scott[75%]	30 hrs	
31	LEXEVS-669	100%	Latest Version of SNOMEDCT Does not load transitivity table	2 wks	30	Fri 10/17/14	Fri 10/31/14	Scott[75%]	60 hrs	
32	LEXEVS-667	100%	TreeService getTree method fails on remote call when the root node code appears in multiple namespaces.	2 wks	31	Fri 10/31/14	Fri 11/14/14	Scott[75%]	60 hrs	
33	LEXEVS-680	100%	Remove GEM loader documentation	1 hr	32	Fri 11/14/14	Fri 11/14/14	Scott[75%]	0.75 hrs	
34		75%	<b>OWL2 Development</b>	<b>20 days</b>		<b>Fri 11/14/14</b>	<b>Mon 12/15/14</b>		<b>120 hrs</b>	
35		75%	OWL2 Design Discussions	4 wks	33	Fri 11/14/14	Mon 12/15/14	Scott[75%]	120 hrs	
36	LEXEVS-679	0%	Expand loader documentation to include creating, running, and errors information.	1 day	33,34	Mon 12/15/14	Tue 12/16/14	Scott[75%]	6 hrs	
37	LEXEVSCTS2-8	100%	UI - Only 50 entries are returned for value sets that have more than 50 entries	1 hr	27FS+4 wks	Mon 11/17/14	Mon 11/17/14	Cory[50%]	0.5 hrs	
38	LEXEVSCTS2-21	75%	Value Set resolution fails when a value set name is more than a particular number of characters.	3 days	37	Mon 11/17/14	Wed 12/10/14	Cory[50%]	12 hrs	
39	LEXEVSCTS2-27	0%	Create interactive CTS2 API documentation	2 days	38	Wed 12/10/14	Fri 12/12/14	Cory[50%]	8 hrs	
40	LEXEVSCTS2-28	0%	NLM (VSAC) CTS2 Service authentication is failing	2 days	39	Fri 12/12/14	Tue 12/16/14	Cory[50%]	8 hrs	
41		0%	Milestone: JIRA Item Development Complete	0 days	29	Tue 12/16/14	Tue 12/16/14		0 hrs	
42		0%	Milestone - Maintenance and Support Development Complete	0 days	25	Tue 12/16/14	Tue 12/16/14		0 hrs	
43		0%	<b>Update Technical Documentation</b>	<b>14 days</b>	<b>25</b>	<b>Tue 12/23/14</b>	<b>Wed 1/14/15</b>		<b>120 hrs</b>	
44		0%	Project Closure	2 days	25FS+1 wk	Tue 12/23/14	Tue 12/30/14	Craig[25%],Scott[75%],Co	24 hrs	
45		0%	Design and Architecture Guide	4 days	44	Tue 12/30/14	Tue 1/6/15	Scott[75%],Cory[50%]	36 hrs	
46		0%	Programmer's Guide	2 days	45	Tue 1/6/15	Thu 1/8/15	Scott[75%],Cory[50%]	20 hrs	
47		0%	Install Guide	2 days	46	Thu 1/8/15	Mon 1/12/15	Scott[75%],Cory[50%]	20 hrs	
48		0%	Administrator Guide	2 days	47	Mon 1/12/15	Wed 1/14/15	Scott[75%],Cory[50%]	20 hrs	
49		0%	Milestone: Update Technical Documentation Complete	0 days	43	Wed 1/14/15	Wed 1/14/15		0 hrs	

S13-500 MOD4 LexEVS Project Plan

ID	JIRA#	% Complete	Task Name	Duration	Predecessor	Start	Finish	Resource Names	Work
50		0%	<b>Operational Readiness Review</b>	4.5 days	25FS+1 wk	Tue 12/23/14	Wed 12/31/14		5 hrs
51		0%	Create Operational Readiness Review Package	4 days		Tue 12/23/14	Tue 12/30/14	Craig[25%]	4 hrs
52		0%	Submit Rediness Review Package to COTR for review.	4 hrs	51	Tue 12/30/14	Wed 12/31/14	Craig[25%]	1 hr
53		0%	<b>Milestone: Operational Readiness Review Complete</b>	0 hrs	50	Wed 12/31/14	Wed 12/31/14		0 hrs
54		0%	<b>Tier Deployment at NCI</b>	10.11 days		Tue 12/16/14	Wed 12/31/14		168.5 hrs
55		0%	<b>Dev Deployment</b>	2 days	25	Tue 12/16/14	Thu 12/18/14		60 hrs
56		0%	Deploy Updated LexEVS 6.3	2 days		Tue 12/16/14	Thu 12/18/14	Scott[75%],Cory[50%]	20 hrs
57		0%	Deploy Updated LexEVS 6.3 CTS2 Service	2 days		Tue 12/16/14	Thu 12/18/14	Scott[75%],Cory[50%]	20 hrs
58		0%	Deploy Updated LexEVS 6.3 URI Resolver Service	2 days		Tue 12/16/14	Thu 12/18/14	Scott[75%],Cory[50%]	20 hrs
59		0%	<b>On Site Deployment</b>	3.11 days	55	Thu 12/18/14	Tue 12/23/14		56 hrs
60		0%	QA Deployment	1.11 days	55	Thu 12/18/14	Fri 12/19/14	Scott[75%],Cory[50%],NC	20 hrs
61		0%	Stage Deployment	2 days	60	Fri 12/19/14	Tue 12/23/14	Scott[75%],Cory[50%],NC	36 hrs
62		0%	Production Deployment	1 wk	59	Tue 12/23/14	Wed 12/31/14	NCI Resource	40 hrs
63		0%	<b>Product Communication</b>	3 days		Tue 12/23/14	Mon 12/29/14		12.5 hrs
64		0%	Release Notes	2 hrs	59	Tue 12/23/14	Tue 12/23/14	Scott[75%],Cory[50%]	2.5 hrs
65		0%	Announcement	1 day	59	Tue 12/23/14	Mon 12/29/14	Scott[75%],Cory[50%]	10 hrs
66		0%	<b>Milestone: Tier Deployment at NCI</b>	0 days	54	Wed 12/31/14	Wed 12/31/14		0 hrs
67		0%	<b>Close</b>	2.8 days	59	Tue 12/23/14	Mon 12/29/14		5.4 hrs
68		0%	Lessons Learned	4 hrs		Tue 12/23/14	Mon 12/29/14	Craig[25%],Scott[75%],Co	3 hrs
69		0%	<b>Deliverable: Project Summary</b>	0.3 days	68	Mon 12/29/14	Mon 12/29/14		2.4 hrs
70		0%	<b>Milestone: S13-500 MOD4 LexEVS Project Plan Complete</b>	0 days	54	Wed 12/31/14	Wed 12/31/14		0 hrs

S13-500 MOD4 LexEVS Project Plan

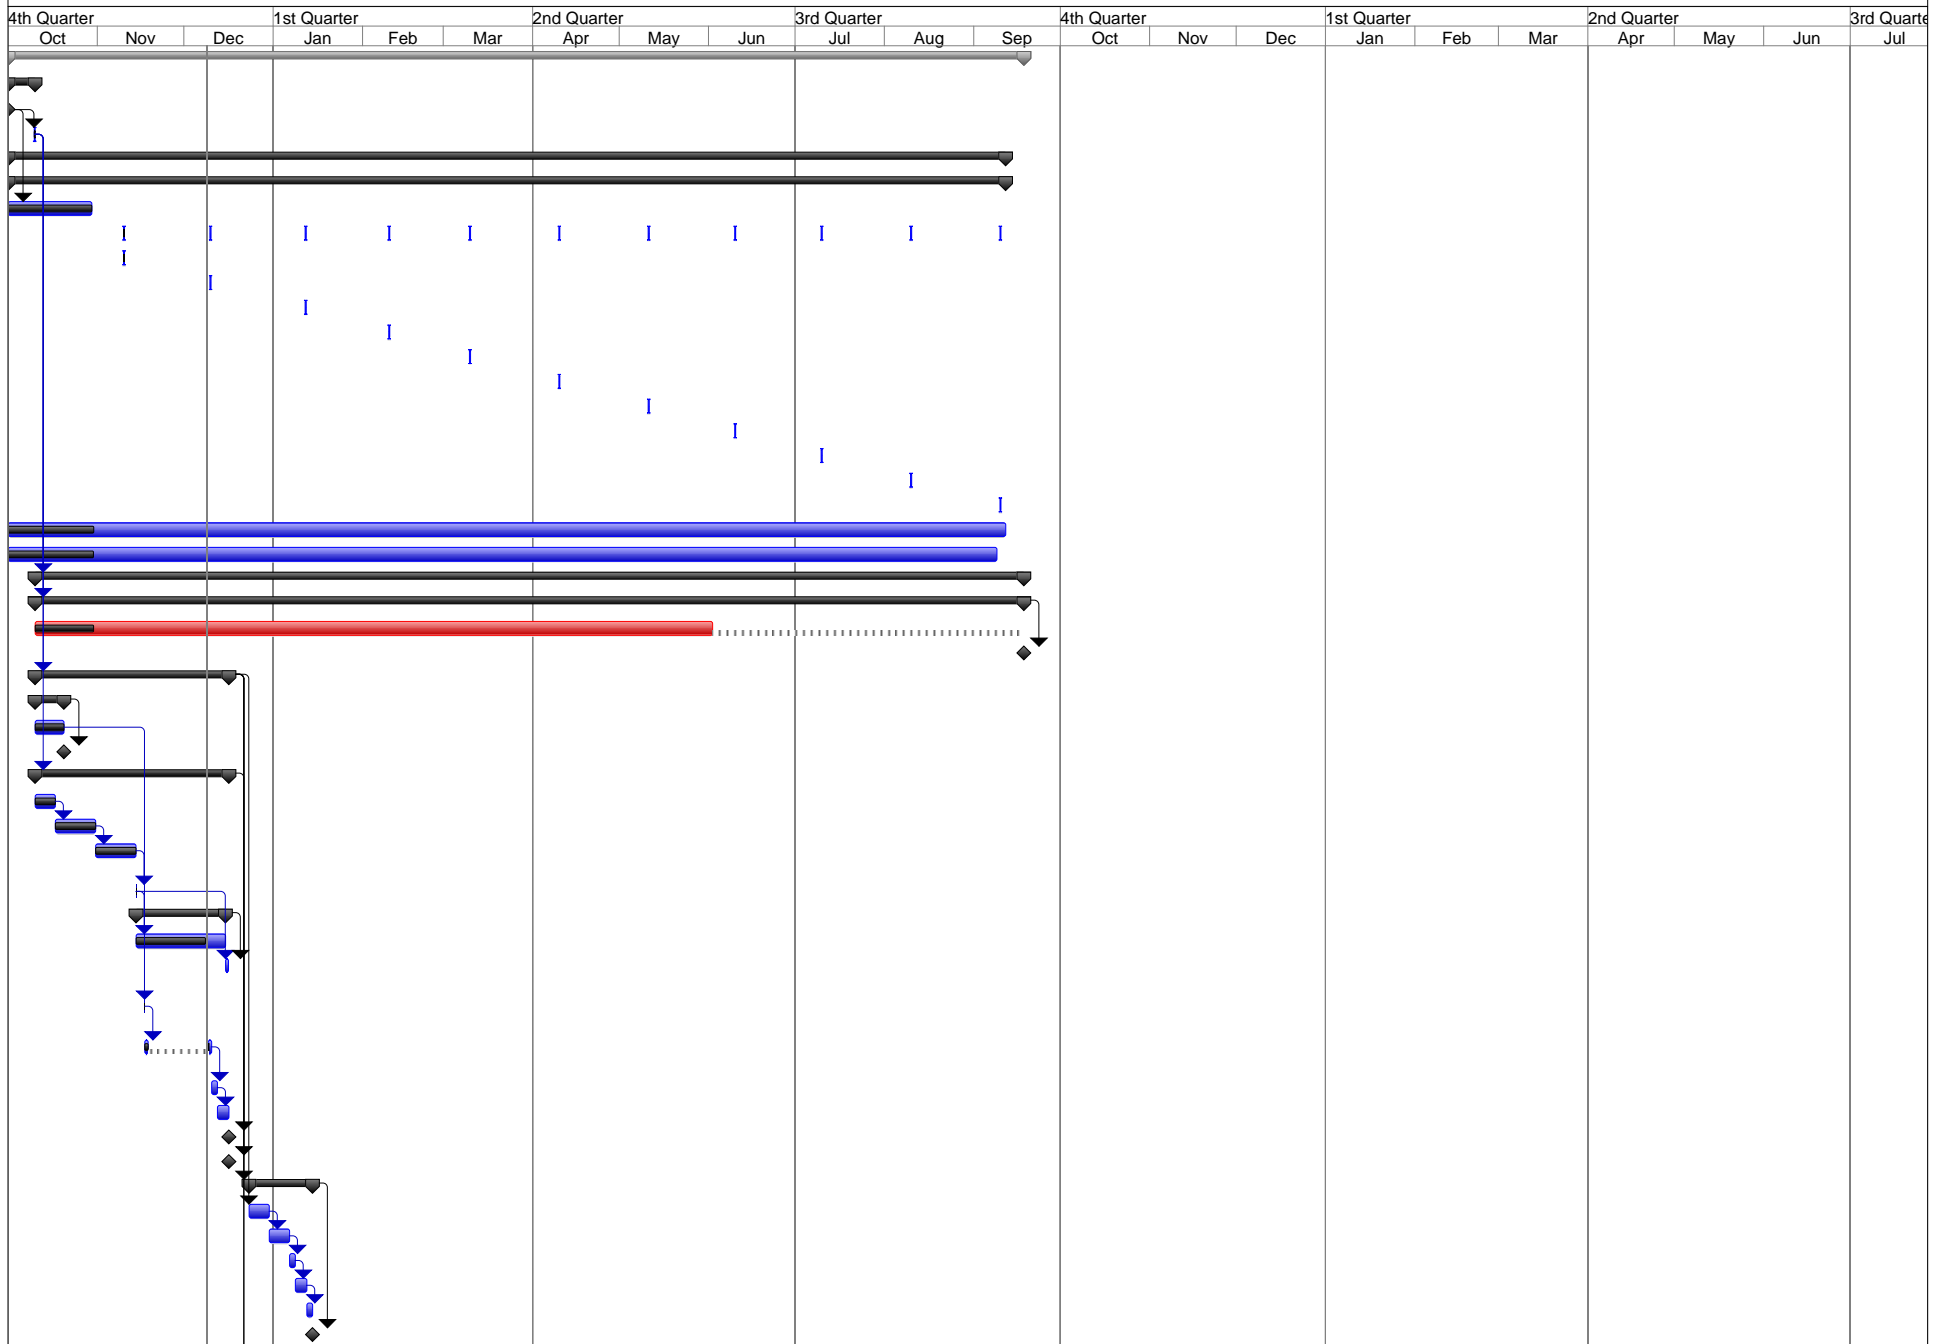

S13-500 MOD4 LexEVS Project Plan

