


S13-500 MOD4 LexEVS Project Plan

ID	JIRA#	% Complete	Task Name	Duration	Predecessor	Start	Finish	Resource Names	Work
0		24%	S13-500 MOD4 LexEVS Project Plan	247.13 days?		Wed 10/1/14	Fri 9/18/15		1,421.15 hrs
1		100%	Initiate	7.13 days		Wed 10/1/14	Fri 10/10/14		3 hrs
2		100%	Contract Sign-off	0 days		Wed 10/1/14	Wed 10/1/14		0 hrs
3		100%	Project Kick-off	1 hr	2FS+7 days	Fri 10/10/14	Fri 10/10/14	Craig,Scott,Cory	3 hrs
4		20%	Planning & Control	243 days		Wed 10/1/14	Fri 9/11/15		252 hrs
5		20%	Project Management	243 days		Wed 10/1/14	Fri 9/11/15		252 hrs
6		100%	Update Project Wiki	21 days	2	Wed 10/1/14	Wed 10/29/14	Craig[5%]	8 hrs
7		18%	Monthly Status & Financial Reporting	213.13 days		Mon 11/10/14	Thu 9/10/15		22 hrs
8		100%	Monthly Status & Financial Reporting 1	1 hr		Mon 11/10/14	Mon 11/10/14	Craig,Scott	2 hrs
9		100%	Monthly Status & Financial Reporting 2	1 hr		Wed 12/10/14	Wed 12/10/14	Craig,Scott	2 hrs
10		0%	Monthly Status & Financial Reporting 3	1 hr		Mon 1/12/15	Mon 1/12/15	Craig,Scott	2 hrs
11		0%	Monthly Status & Financial Reporting 4	1 hr		Tue 2/10/15	Tue 2/10/15	Craig,Scott	2 hrs
12		0%	Monthly Status & Financial Reporting 5	1 hr		Tue 3/10/15	Tue 3/10/15	Craig,Scott	2 hrs
13		0%	Monthly Status & Financial Reporting 6	1 hr		Fri 4/10/15	Fri 4/10/15	Craig,Scott	2 hrs
14		0%	Monthly Status & Financial Reporting 7	1 hr		Mon 5/11/15	Mon 5/11/15	Craig,Scott	2 hrs
15		0%	Monthly Status & Financial Reporting 8	1 hr		Wed 6/10/15	Wed 6/10/15	Craig,Scott	2 hrs
16		0%	Monthly Status & Financial Reporting 9	1 hr		Fri 7/10/15	Fri 7/10/15	Craig,Scott	2 hrs
17		0%	Monthly Status & Financial Reporting 10	1 hr		Mon 8/10/15	Mon 8/10/15	Craig,Scott	2 hrs
18		0%	Monthly Status & Financial Reporting 11	1 hr		Thu 9/10/15	Thu 9/10/15	Craig,Scott	2 hrs
19		17%	Ongoing Project Management	12 mons		Wed 10/1/14	Fri 9/11/15	Craig[2%]	30 hrs
20		17%	Ongoing Project Oversight	12 mons		Wed 10/1/14	Tue 9/8/15	Dr. Chute[10%]	192 hrs
21		28%	Execute	240 days?	3	Fri 10/10/14	Fri 9/18/15		1,160.75 hrs
22		17%	Ongoing Operational Support	240 days	3	Fri 10/10/14	Fri 9/18/15		400 hrs
23		17%	Tech Support/Forum Management/Ongoing Technical Expertise	12 mons		Fri 10/10/14	Fri 9/18/15	Scott[25%]	400 hrs
24		0%	Milestone: Ongoing Operational Support Complete	0 days	22	Fri 9/18/15	Fri 9/18/15		0 hrs
25		68%	Maintenance and Support Development	61.13 days?	3	Fri 10/10/14	Thu 1/8/15		467.25 hrs
26		100%	Supporting Item Development	6 days		Fri 10/10/14	Mon 10/20/14		20 hrs
27		100%	AMIA Poster	1 wk		Fri 10/10/14	Mon 10/20/14	Cory[50%]	20 hrs
28		100%	Milestone:Supporting Item Development Complete	0 days	26	Mon 10/20/14	Mon 10/20/14		0 hrs
29		66%	JIRA Item Development	61.13 days?	3	Fri 10/10/14	Thu 1/8/15		447.25 hrs
30	LEXEVS-671	100%	SNOMEDCT does not load hierarchy or root nodes.	1 wk		Fri 10/10/14	Fri 10/17/14	Scott[75%]	30 hrs
31	LEXEVS-669	100%	Latest Version of SNOMEDCT Does not load transitivity table	2 wks	30	Fri 10/17/14	Fri 10/31/14	Scott[75%]	60 hrs
32	LEXEVS-667	100%	TreeService getTree method fails on remote call when the root node code appears in multiple namespaces.	2 wks	31	Fri 10/31/14	Fri 11/14/14	Scott[75%]	60 hrs
33	LEXEVS-598	100%	TreeService getTree method can fail when the root node code appears in multiple namespaces.	1 wk	32	Fri 11/14/14	Fri 11/21/14	Scott[75%]	30 hrs
34	LEXEVS-680	100%	Remove GEM loader documentation	1 hr	33	Fri 11/14/14	Fri 11/14/14	Scott[75%]	0.75 hrs
35		67%	OWL2 Development	50.13 days?		Fri 10/10/14	Mon 12/22/14		174 hrs
36		72%	OWL2 Design Discussions	5 wks	34	Fri 11/14/14	Mon 12/22/14	Scott[75%]	150 hrs
37	LEXEVS-641	100%	OWL2 loader uses VersionIRI, but doesn't have a wide enough column	4 hrs	34	Fri 11/14/14	Fri 11/14/14	Scott[75%]	3 hrs
38	LEXEVS-614	100%	OWL2 associations and annotations on associations.	3.5 days	37	Fri 11/14/14	Thu 11/20/14	Scott[75%]	21 hrs
39	LEXEVS-583	0%	OWL2 data: restrictions on a class using datatype properties	1 day?		Fri 10/10/14	Mon 10/13/14		0 hrs
40	LEXEVS-586	0%	OWL2 chained properties	1 day?		Fri 10/10/14	Mon 10/13/14		0 hrs
41	LEXEVS-643	0%	OWL2 test files	1 day?		Fri 10/10/14	Mon 10/13/14		0 hrs
42	LEXEVS-595	0%	Need a Method to Identify OWL Resources in an Unstructured environment	1 day?		Fri 10/10/14	Mon 10/13/14		0 hrs
43	LEXEVS-679	0%	Expand loader documentation to include creating, running, and errors information.	1 day	34,35	Mon 12/22/14	Tue 12/23/14	Scott[75%]	6 hrs
44	LEXEVSCTS2-8	100%	UI - Only 50 entries are returned for value sets that have more than 50 entries	1 hr	27FS+4 wks	Mon 11/17/14	Mon 11/17/14	Cory[50%]	0.5 hrs
45	LEXEVSCTS2-21	75%	Value Set resolution fails when a value set name is more than a particular number of characters.	3 days	44	Mon 11/17/14	Wed 12/10/14	Cory[50%]	12 hrs
46	LEXEVSCTS2-27	0%	Create interactive CTS2 API documentation	2 days	45	Wed 12/10/14	Fri 12/12/14	Cory[50%]	8 hrs
47	LEXEVSCTS2-28	0%	NLM (VSAC) CTS2 Service authentication is failing	2 days	46	Fri 12/12/14	Tue 12/16/14	Cory[50%]	8 hrs

S13-500 MOD4 LexEVS Project Plan

ID	JIRA#	% Complete	Task Name	Duration	Predecessors	Start	Finish	Resource Names	Work	Sep
48	LEXEVS-581	0%	LexEVSValueSetDefinitionServicesImpl exportValueSetResolution method could fail.	2 days	47	Tue 12/16/14	Thu 12/18/14	Cory[50%]	8 hrs	
49	LEXEVS-636	0%	LexEVSValueSetDefinitionServices exportValueSetResolution method returns unprocessable InputStream.	2 days	47	Tue 12/16/14	Thu 12/18/14	Cory[50%]	8 hrs	
50	LEXEVS-601	0%	Update resumeBatch to cover more kinds of failures	1 wk	43	Tue 12/23/14	Tue 1/6/15	Scott[75%]	30 hrs	
51	LEXEVS-623	0%	Mapping extension search methods fail on distributed mode.	2 days	50	Tue 1/6/15	Thu 1/8/15	Scott[75%]	12 hrs	
52		0%	Milestone: JIRA Item Development Complete	0 days	29	Thu 1/8/15	Thu 1/8/15		0 hrs	
53		0%	Milestone - Maintenance and Support Development Complete	0 days	25	Thu 1/8/15	Thu 1/8/15		0 hrs	
54		0%	Update Technical Documentation	12 days	25	Thu 1/15/15	Mon 2/2/15		120 hrs	
55		0%	Project Closure	2 days	25FS+1 wk	Thu 1/15/15	Mon 1/19/15	Craig[25%],Scott[75%],Co	24 hrs	
56		0%	Design and Architecture Guide	4 days	55	Mon 1/19/15	Fri 1/23/15	Scott[75%],Cory[50%]	36 hrs	
57		0%	Programmer's Guide	2 days	56	Fri 1/23/15	Tue 1/27/15	Scott[75%],Cory[50%]	20 hrs	
58		0%	Install Guide	2 days	57	Tue 1/27/15	Thu 1/29/15	Scott[75%],Cory[50%]	20 hrs	
59		0%	Administrator Guide	2 days	58	Thu 1/29/15	Mon 2/2/15	Scott[75%],Cory[50%]	20 hrs	
60		0%	Milestone: Update Technical Documentation Complete	0 days	54	Mon 2/2/15	Mon 2/2/15		0 hrs	
61		0%	Operational Readiness Review	4.5 days	25FS+1 wk	Thu 1/15/15	Wed 1/21/15		5 hrs	
62		0%	Create Operational Readiness Review Package	4 days		Thu 1/15/15	Wed 1/21/15	Craig[25%]	4 hrs	
63		0%	Submit Rediness Review Package to COTR for review.	4 hrs	62	Wed 1/21/15	Wed 1/21/15	Craig[25%]	1 hr	
64		0%	Milestone: Operational Readiness Review Complete	0 hrs	61	Wed 1/21/15	Wed 1/21/15		0 hrs	
65		0%	Tier Deployment at NCI	10.11 days		Thu 1/8/15	Thu 1/22/15		168.5 hrs	
66		0%	Dev Deployment	2 days	25	Thu 1/8/15	Mon 1/12/15		60 hrs	
67		0%	Deploy Updated LexEVS 6.3	2 days		Thu 1/8/15	Mon 1/12/15	Scott[75%],Cory[50%]	20 hrs	
68		0%	Deploy Updated LexEVS 6.3 CTS2 Service	2 days		Thu 1/8/15	Mon 1/12/15	Scott[75%],Cory[50%]	20 hrs	
69		0%	Deploy Updated LexEVS 6.3 URI Resolver Service	2 days		Thu 1/8/15	Mon 1/12/15	Scott[75%],Cory[50%]	20 hrs	
70		0%	On Site Deployment	3.11 days	66	Mon 1/12/15	Thu 1/15/15		56 hrs	
71		0%	QA Deployment	1.11 days	66	Mon 1/12/15	Tue 1/13/15	Scott[75%],Cory[50%],NC	20 hrs	
72		0%	Stage Deployment	2 days	71	Tue 1/13/15	Thu 1/15/15	Scott[75%],Cory[50%],NC	36 hrs	
73		0%	Production Deployment	1 wk	70	Thu 1/15/15	Thu 1/22/15	NCI Resource	40 hrs	
74		0%	Product Communication	1 day		Thu 1/15/15	Fri 1/16/15		12.5 hrs	
75		0%	Release Notes	2 hrs	70	Thu 1/15/15	Thu 1/15/15	Scott[75%],Cory[50%]	2.5 hrs	
76		0%	Announcement	1 day	70	Thu 1/15/15	Fri 1/16/15	Scott[75%],Cory[50%]	10 hrs	
77		0%	Milestone: Tier Deployment at NCI	0 days	65	Thu 1/22/15	Thu 1/22/15		0 hrs	
78		0%	Close	0.8 days	70	Thu 1/15/15	Fri 1/16/15		5.4 hrs	
79		0%	Lessons Learned	4 hrs		Thu 1/15/15	Thu 1/15/15	Craig[25%],Scott[75%],Co	3 hrs	
80		0%	Deliverable: Project Summary	0.3 days	79	Thu 1/15/15	Fri 1/16/15		2.4 hrs	
81		0%	Milestone: S13-500 MOD4 LexEVS Project Plan Complete	0 days	65	Thu 1/22/15	Thu 1/22/15		0 hrs	

S13-500 MOD4 LexEVS Project Plan

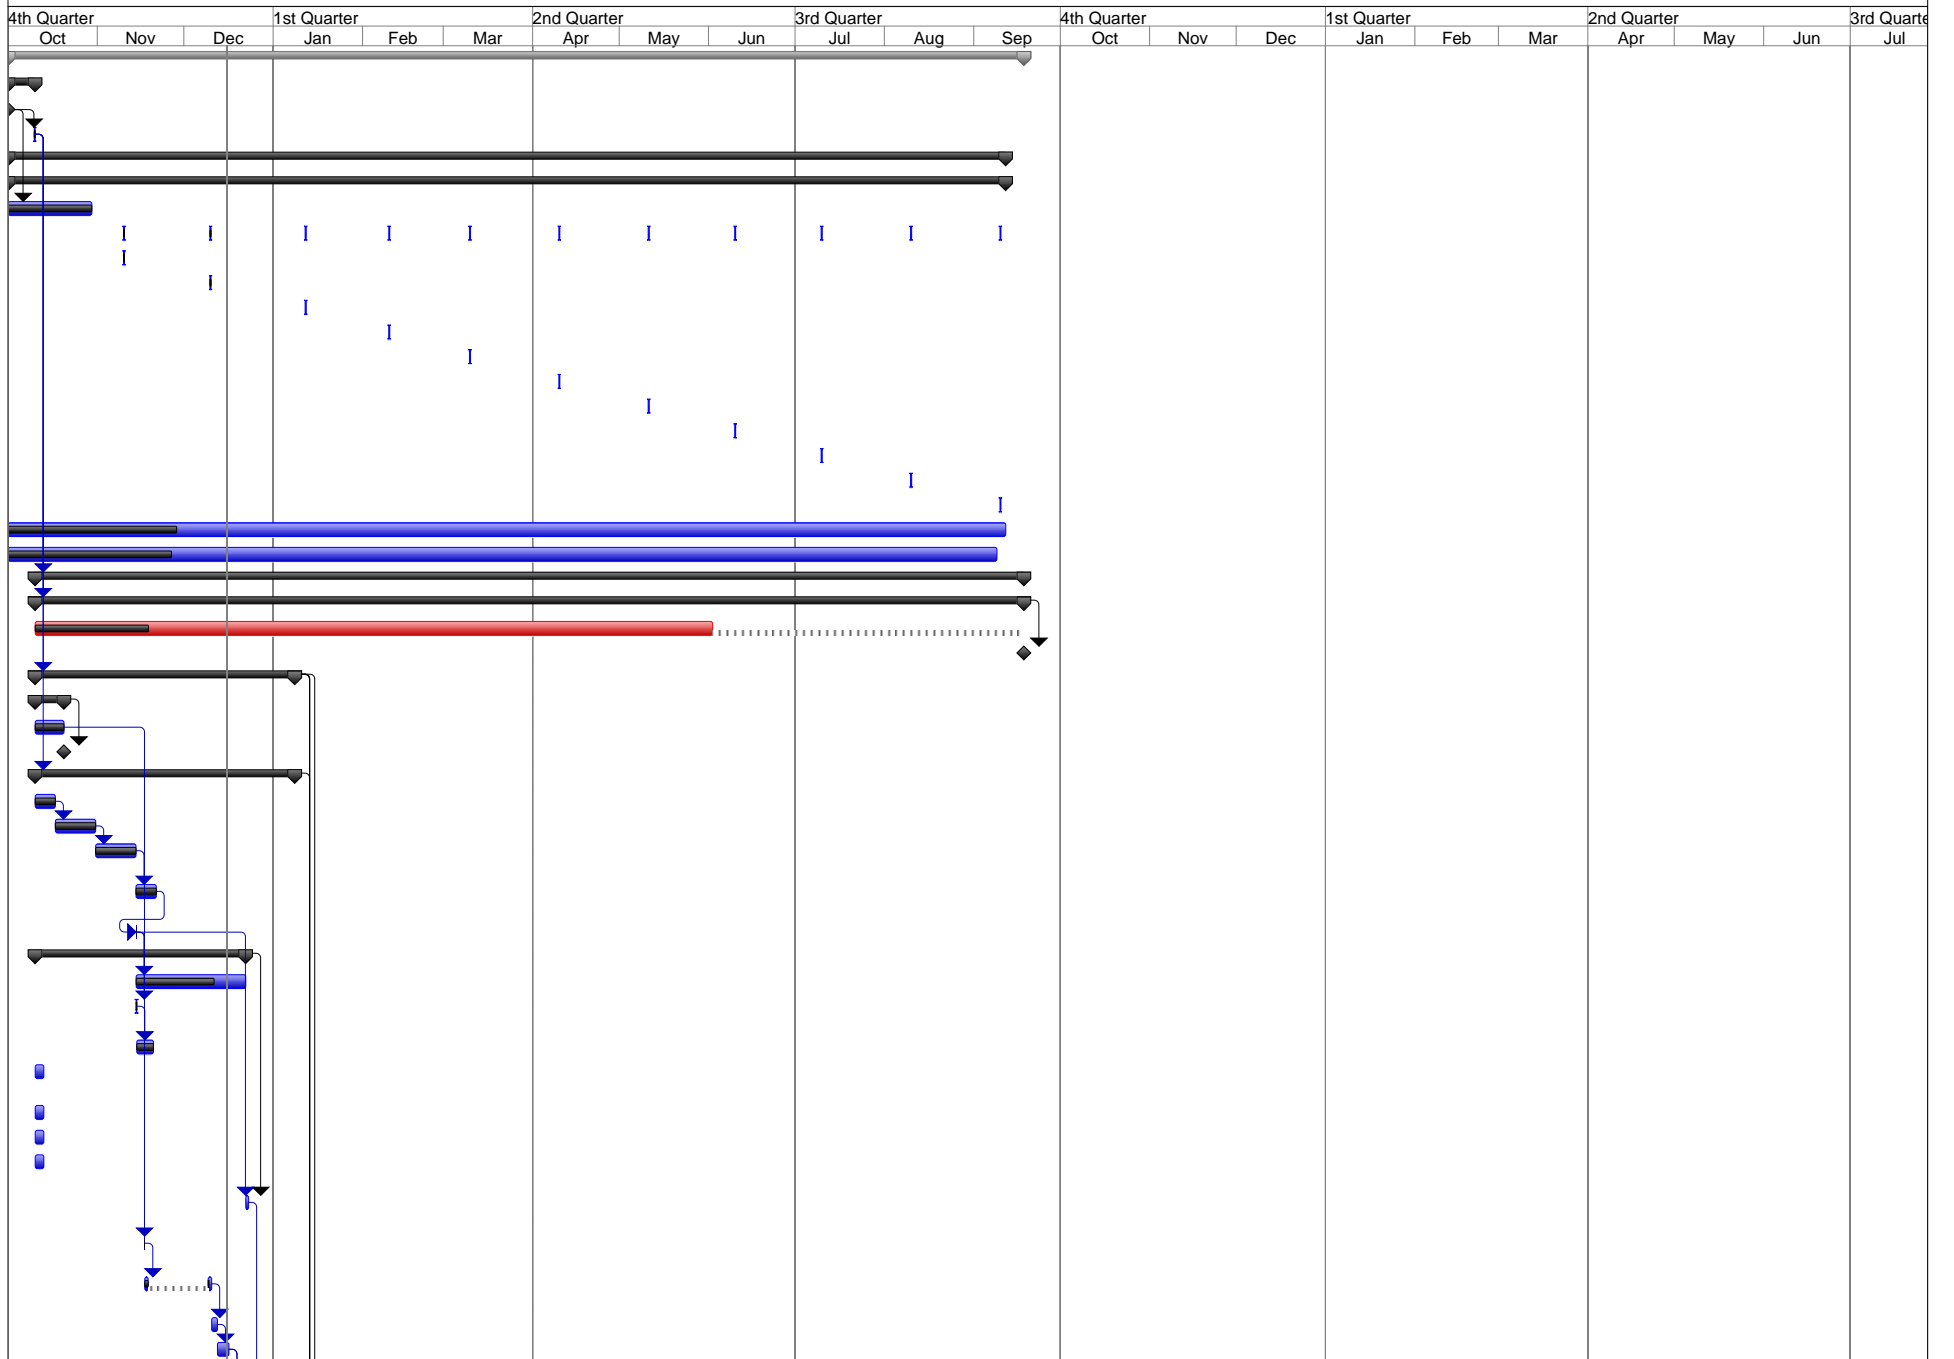

S13-500 MOD4 LexEVS Project Plan

