


S13-500 MOD4 LexEVS Project Plan

ID	JIRA#	% Complete	Task Name	Duration	Predecessors	Start	Finish	Resource Names	Work
0		29%	S13-500 MOD4 LexEVS Project Plan	247.13 days		Wed 10/1/14	Fri 9/18/15		1,687.15 hrs
1		100%	Initiate	7.13 days		Wed 10/1/14	Fri 10/10/14		3 hrs
2		100%	Contract Sign-off	0 days		Wed 10/1/14	Wed 10/1/14		0 hrs
3		100%	Project Kick-off	1 hr	2FS+7 days	Fri 10/10/14	Fri 10/10/14	Craig,Scott,Cory	3 hrs
4		20%	Planning & Control	243 days		Wed 10/1/14	Fri 9/11/15		252 hrs
5		20%	Project Management	243 days		Wed 10/1/14	Fri 9/11/15		252 hrs
6		100%	Update Project Wiki	21 days	2	Wed 10/1/14	Wed 10/29/14	Craig[5%]	8 hrs
7		27%	Monthly Status & Financial Reporting	213.13 days		Mon 11/10/14	Thu 9/10/15		22 hrs
8		100%	Monthly Status & Financial Reporting 1	1 hr		Mon 11/10/14	Mon 11/10/14	Craig,Scott	2 hrs
9		100%	Monthly Status & Financial Reporting 2	1 hr		Wed 12/10/14	Wed 12/10/14	Craig,Scott	2 hrs
10		100%	Monthly Status & Financial Reporting 3	1 hr		Mon 1/12/15	Mon 1/12/15	Craig,Scott	2 hrs
11		0%	Monthly Status & Financial Reporting 4	1 hr		Tue 2/10/15	Tue 2/10/15	Craig,Scott	2 hrs
12		0%	Monthly Status & Financial Reporting 5	1 hr		Tue 3/10/15	Tue 3/10/15	Craig,Scott	2 hrs
13		0%	Monthly Status & Financial Reporting 6	1 hr		Fri 4/10/15	Fri 4/10/15	Craig,Scott	2 hrs
14		0%	Monthly Status & Financial Reporting 7	1 hr		Mon 5/11/15	Mon 5/11/15	Craig,Scott	2 hrs
15		0%	Monthly Status & Financial Reporting 8	1 hr		Wed 6/10/15	Wed 6/10/15	Craig,Scott	2 hrs
16		0%	Monthly Status & Financial Reporting 9	1 hr		Fri 7/10/15	Fri 7/10/15	Craig,Scott	2 hrs
17		0%	Monthly Status & Financial Reporting 10	1 hr		Mon 8/10/15	Mon 8/10/15	Craig,Scott	2 hrs
18		0%	Monthly Status & Financial Reporting 11	1 hr		Thu 9/10/15	Thu 9/10/15	Craig,Scott	2 hrs
19		17%	Ongoing Project Management	12 mons		Wed 10/1/14	Fri 9/11/15	Craig[2%]	30 hrs
20		17%	Ongoing Project Oversight	12 mons		Wed 10/1/14	Tue 9/8/15	Dr. Chute[10%]	192 hrs
21		40%	Execute	240 days		Fri 10/10/14	Fri 9/18/15		1,426.75 hrs
22		17%	Ongoing Operational Support	240 days		Fri 10/10/14	Fri 9/18/15		400 hrs
23		17%	Tech Support/Forum Management/Ongoing Technical Expertise	12 mons		Fri 10/10/14	Fri 9/18/15	Scott[25%]	400 hrs
24		0%	Milestone: Ongoing Operational Support Complete	0 days	22	Fri 9/18/15	Fri 9/18/15		0 hrs
25		89%	Maintenance and Support Development	75.46 days		Fri 10/10/14	Wed 1/28/15		785.25 hrs
26		100%	Supporting Item Development	6 days		Mon 10/20/14	Mon 10/20/14		20 hrs
28		100%	Milestone: Supporting Item Development Complete	0 days	26	Mon 10/20/14	Mon 10/20/14		0 hrs
29		10%	6.2 Deployment Tasks	5 days		Mon 1/12/15	Mon 1/19/15		30 hrs
30		10%	Deployment Tasks	5 days	44	Mon 1/12/15	Mon 1/19/15	Scott[75%]	30 hrs
31		92%	JIRA Item Development	75.46 days		Fri 10/10/14	Wed 1/28/15		735.25 hrs
32	LEXEVS-671	100%	SNOMEDCT does not load hierarchy or root nodes.	1 wk		Fri 10/10/14	Fri 10/17/14	Scott[75%]	30 hrs
33	LEXEVS-669	100%	Latest Version of SNOMEDCT Does not load transitivity table	2 wks	32	Fri 10/17/14	Fri 10/31/14	Scott[75%]	60 hrs
34	LEXEVS-667	100%	TreeService getTree method fails on remote call when the root node code appears in multiple namespaces.	2 wks	33	Fri 10/31/14	Fri 11/14/14	Scott[75%]	60 hrs
35	LEXEVS-598	100%	TreeService getTree method can fail when the root node code appears in multiple namespaces.	1 wk	34	Fri 11/14/14	Fri 11/21/14	Scott[75%]	30 hrs
36	LEXEVS-680	100%	Remove GEM loader documentation	1 hr	35	Fri 11/14/14	Fri 11/14/14	Scott[75%]	0.75 hrs
37		91%	OWL2 Development	50.33 days		Fri 11/14/14	Wed 1/28/15		454 hrs
38		100%	OWL2 Design Discussions	5 wks	36	Fri 11/14/14	Mon 12/22/14	Scott[75%]	150 hrs
39	LEXEVS-641	100%	OWL2 loader uses VersionIRI, but doesn't have a wide enough column	4 hrs	36	Fri 11/14/14	Fri 11/14/14	Scott[75%]	3 hrs
40	LEXEVS-614	100%	OWL2 associations and annotations on associations.	3.5 days	39	Fri 11/14/14	Thu 11/20/14	Scott[75%]	21 hrs
41	LEXEVS-684	100%	OWL2 Loader does not properly Parse output from render	10 days	40	Thu 11/20/14	Fri 12/5/14	Scott[75%]	60 hrs
42	LEXEVS-685	100%	OWL2 Loader loads disJointWith association as equivalent class	10 days	41	Fri 12/5/14	Fri 12/19/14	Scott[75%]	60 hrs
43	LEXEVS-583	100%	OWL2 data: restrictions on a class using datatype properties	6.67 days	42	Fri 12/19/14	Mon 1/5/15	Scott[75%]	40 hrs
44		100%	OWL Evaluation	2 wks	43	Mon 1/5/15	Mon 1/19/15	NCI Resource	80 hrs
45		0%	OWL Updates	1.33 wks	44	Mon 1/19/15	Wed 1/28/15	Scott[75%]	40 hrs
46	LEXEVS-623	100%	Mapping extension search methods fail on distributed mode.	6.67 days	36	Tue 12/23/14	Thu 1/8/15	Scott[75%]	40 hrs
47	LEXEVS-679	100%	Expand loader documentation to include creating, running, and errors information.	2.67 days	44	Mon 1/12/15	Thu 1/15/15	Scott[75%]	16 hrs
48	LEXEVSCTS2-8	100%	UI - Only 50 entries are returned for value sets that have more than 50 entries	1 hr	27FS+4 wks	Mon 11/17/14	Mon 11/17/14	Cory[50%]	0.5 hrs

S13-500 MOD4 LexEVS Project Plan

ID	JIRA#	% Complete	Task Name	Duration	Predecessor	Start	Finish	Resource Names	Work	Sep
49	LEXEVSCTS2-21	100%	Value Set resolution fails when a value set name is more than a particular number of characters.	3 days	48	Mon 11/17/14	Wed 12/10/14	Cory[50%]	12 hrs	
50	LEXEVSCTS2-27	100%	Create interactive CTS2 API documentation	1 wk	49	Wed 12/10/14	Wed 12/17/14	Cory[50%]	20 hrs	
51	LEXEVS-636	10%	LexEVSValueSetDefinitionServices exportValueSetResolution method returns unprocessable InputStream.	0.8 wks		Fri 1/16/15	Thu 1/22/15	Kevin[25%]	8 hrs	
52	LEXEVSCTS2-28	100%	NLM (VSAC) CTS2 Service authentication is failing	2 days	43	Mon 1/5/15	Wed 1/7/15	Kevin[25%]	4 hrs	
53		0%	Milestone: JIRA Item Development Complete	0 days	31	Wed 1/28/15	Wed 1/28/15		0 hrs	
54		0%	Milestone - Maintenance and Support Development Complete	0 days	25	Wed 1/28/15	Wed 1/28/15		0 hrs	
55		0%	Update Technical Documentation	8 days	25	Wed 2/4/15	Mon 2/16/15		24 hrs	
56		0%	Project Closure	4 days	25FS+1 wk	Wed 2/4/15	Tue 2/10/15	Craig[25%]	8 hrs	
57		0%	Design and Architecture Guide	1 day	56	Tue 2/10/15	Wed 2/11/15	Cory[50%]	4 hrs	
58		0%	Programmer's Guide	1 day	57	Wed 2/11/15	Thu 2/12/15	Cory[50%]	4 hrs	
59		0%	Install Guide	1 day	58	Thu 2/12/15	Fri 2/13/15	Cory[50%]	4 hrs	
60		0%	Administrator Guide	1 day	59	Fri 2/13/15	Mon 2/16/15	Cory[50%]	4 hrs	
61		0%	Milestone: Update Technical Documentation Complete	0 days	55	Mon 2/16/15	Mon 2/16/15		0 hrs	
62		0%	Operational Readiness Review	4.5 days	25FS+1 wk	Wed 2/4/15	Wed 2/11/15		5 hrs	
63		0%	Create Operational Readiness Review Package	4 days		Wed 2/4/15	Tue 2/10/15	Craig[25%]	4 hrs	
64		0%	Submit Rediness Review Package to COTR for review.	4 hrs	63	Tue 2/10/15	Wed 2/11/15	Craig[25%]	1 hr	
65		0%	Milestone: Operational Readiness Review Complete	0 hrs	62	Wed 2/11/15	Wed 2/11/15		0 hrs	
66		0%	Tier Deployment at NCI	18.69 days		Wed 1/28/15	Tue 2/24/15		212.5 hrs	
67		0%	Dev Deployment	8 days	25	Wed 1/28/15	Mon 2/9/15		80 hrs	
68		0%	Deploy Updated LexEVS 6.3	2 days		Wed 1/28/15	Fri 1/30/15	Scott[75%],Cory[50%]	20 hrs	
69		0%	Deploy Updated LexEVS 6.3 CTS2 Service	2 days	68	Fri 1/30/15	Tue 2/3/15	Scott[75%],Cory[50%]	20 hrs	
70		0%	Deploy Updated LexEVS 6.3 URI Resolver Service	2 days	69	Tue 2/3/15	Thu 2/5/15	Scott[75%],Cory[50%]	20 hrs	
71		0%	Deploy CTS2 API Documentation Service	2 days	70	Thu 2/5/15	Mon 2/9/15	Scott[75%],Cory[50%]	20 hrs	
72		0%	NCI Deployment	4.44 days	67	Mon 2/9/15	Mon 2/16/15		80 hrs	
73		0%	QA Deployment	2.22 days	67	Mon 2/9/15	Wed 2/11/15	Scott[75%],Cory[50%],NC	40 hrs	
74		0%	Stage Deployment	2.22 days	73	Wed 2/11/15	Mon 2/16/15	Scott[75%],Cory[50%],NC	40 hrs	
75		0%	Production Deployment	1 wk	72	Mon 2/16/15	Mon 2/23/15	NCI Resource	40 hrs	
76		0%	Product Communication	1.25 days		Mon 2/23/15	Tue 2/24/15		12.5 hrs	
77		0%	Release Notes	2 hrs	75	Mon 2/23/15	Mon 2/23/15	Scott[75%],Cory[50%]	2.5 hrs	
78		0%	Announcement	1 day	77	Mon 2/23/15	Tue 2/24/15	Scott[75%],Cory[50%]	10 hrs	
79		0%	Milestone: Tier Deployment at NCI	0 days	66	Tue 2/24/15	Tue 2/24/15		0 hrs	
80		0%	Close	0.8 days	66	Tue 2/24/15	Wed 2/25/15		5.4 hrs	
81		0%	Lessons Learned	4 hrs		Tue 2/24/15	Tue 2/24/15	Craig[25%],Scott[75%],Co	3 hrs	
82		0%	Deliverable: Project Summary	0.3 days	81	Tue 2/24/15	Wed 2/25/15		2.4 hrs	
83		0%	Milestone: S13-500 MOD4 LexEVS Project Plan Complete	0 days	66,80	Wed 2/25/15	Wed 2/25/15		0 hrs	

S13-500 MOD4 LexEVS Project Plan

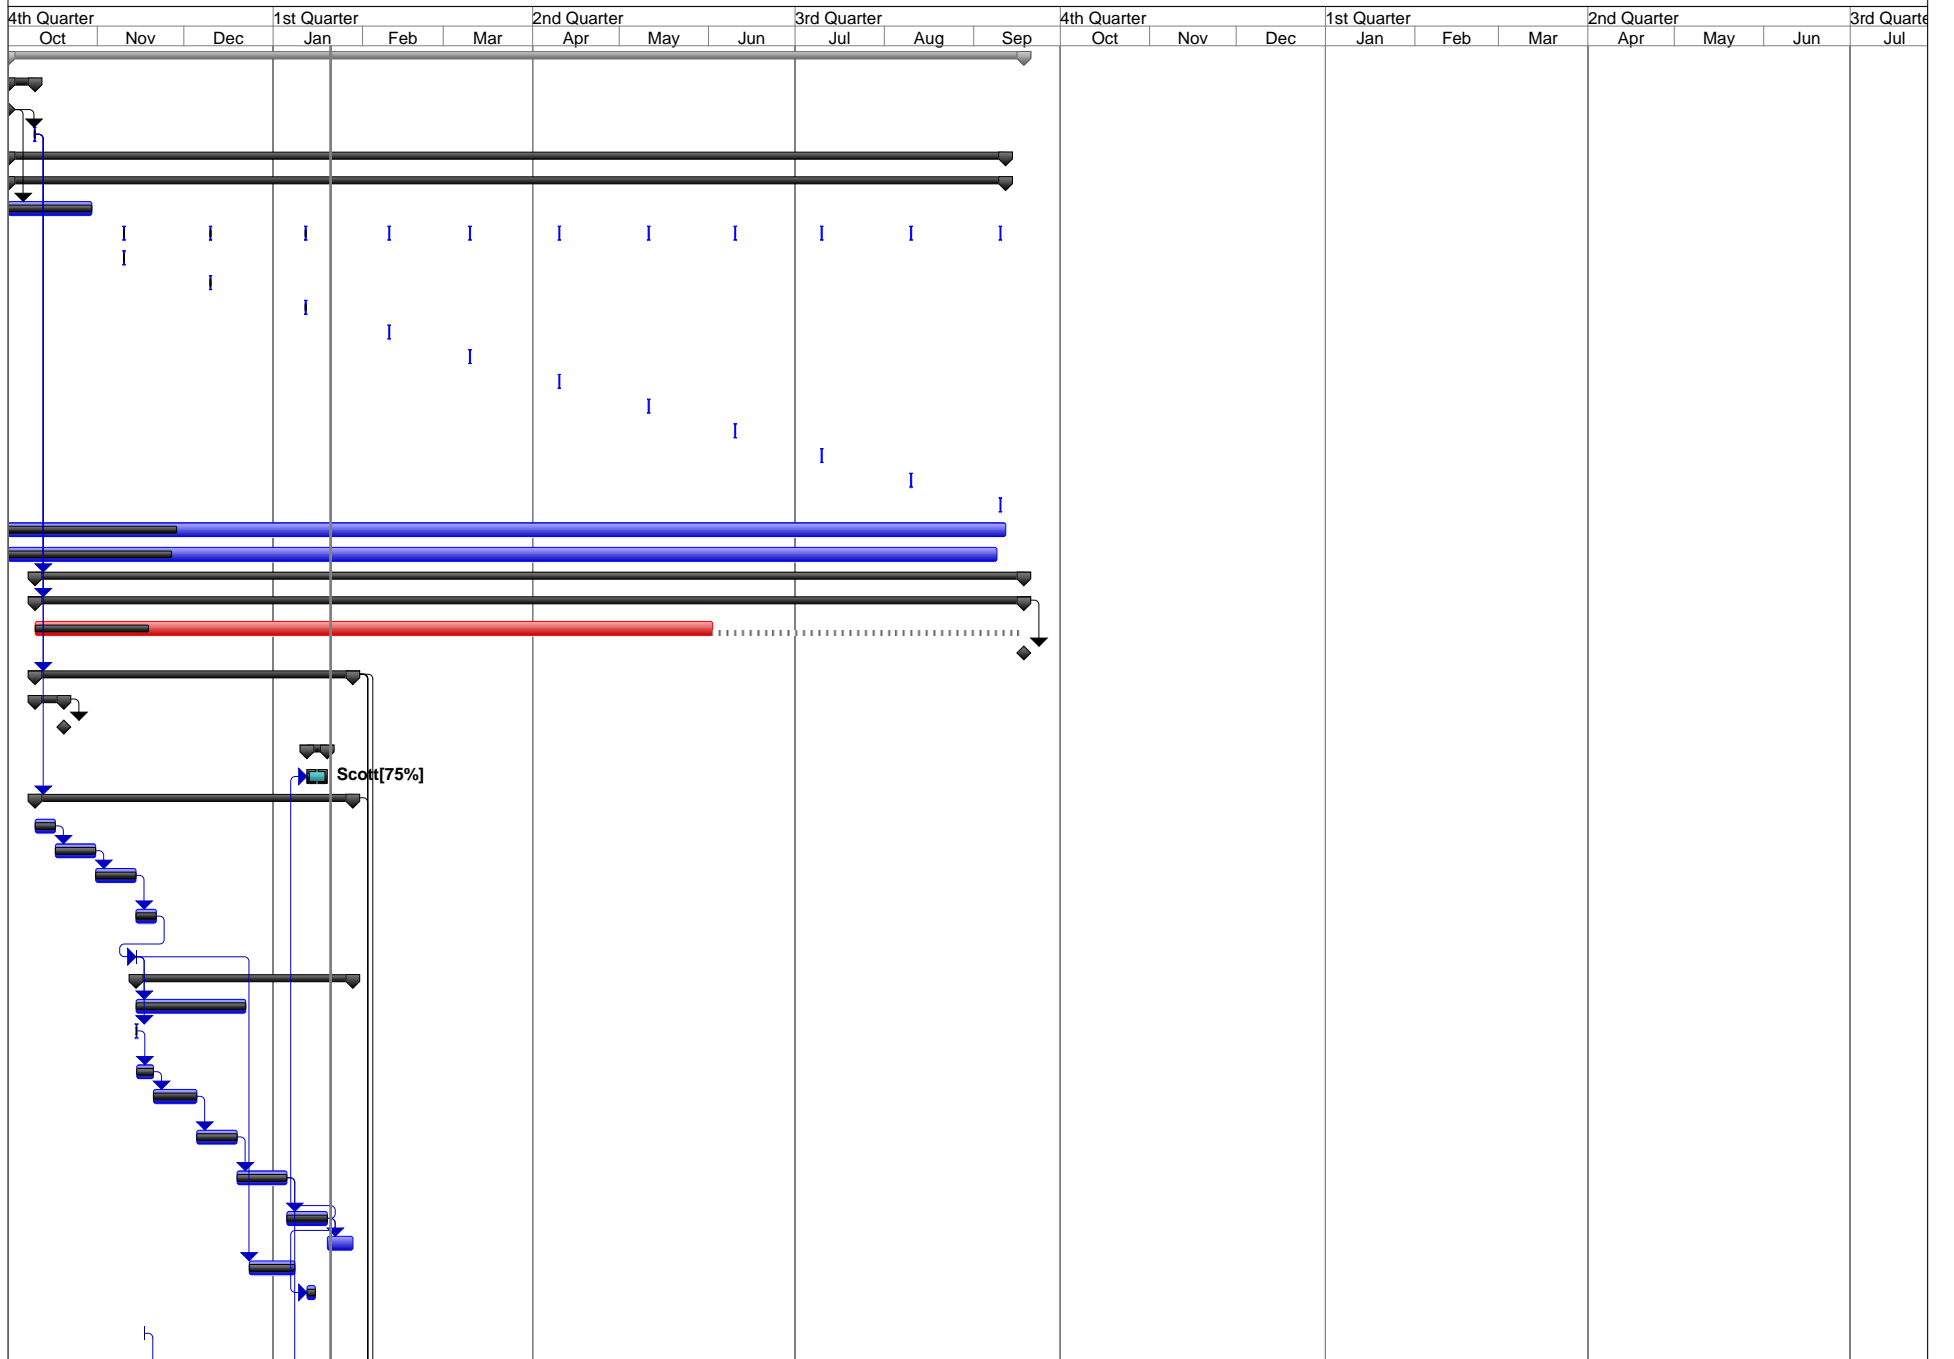

S13-500 MOD4 LexEVS Project Plan

