


S13-500 MOD4 LexEVS Project Plan

ID	JIRA#	% Complete	Task Name	Duration	Predecessors	Start	Finish	Resource Names	Work
0		35%	S13-500 MOD4 LexEVS Project Plan	247.13 days		Wed 10/1/14	Fri 9/18/15		1,854.58 hrs
1		100%	Initiate	7.13 days		Wed 10/1/14	Fri 10/10/14		3 hrs
2		100%	Contract Sign-off	0 days		Wed 10/1/14	Wed 10/1/14		0 hrs
3		100%	Project Kick-off	1 hr	2FS+7 days	Fri 10/10/14	Fri 10/10/14	Craig,Scott,Cory	3 hrs
4		21%	Planning & Control	243 days		Wed 10/1/14	Fri 9/11/15		252 hrs
5		21%	Project Management	243 days		Wed 10/1/14	Fri 9/11/15		252 hrs
6		100%	Update Project Wiki	21 days	2	Wed 10/1/14	Wed 10/29/14	Craig[5%]	8 hrs
7		45%	Monthly Status & Financial Reporting	213.13 days		Mon 11/10/14	Thu 9/10/15		22 hrs
8		100%	Monthly Status & Financial Reporting 1	1 hr		Mon 11/10/14	Mon 11/10/14	Craig,Scott	2 hrs
9		100%	Monthly Status & Financial Reporting 2	1 hr		Wed 12/10/14	Wed 12/10/14	Craig,Scott	2 hrs
10		100%	Monthly Status & Financial Reporting 3	1 hr		Mon 1/12/15	Mon 1/12/15	Craig,Scott	2 hrs
11		100%	Monthly Status & Financial Reporting 4	1 hr		Tue 2/10/15	Tue 2/10/15	Craig,Scott	2 hrs
12		100%	Monthly Status & Financial Reporting 5	1 hr		Tue 3/10/15	Tue 3/10/15	Craig,Scott	2 hrs
13		0%	Monthly Status & Financial Reporting 6	1 hr		Fri 4/10/15	Fri 4/10/15	Craig,Scott	2 hrs
14		0%	Monthly Status & Financial Reporting 7	1 hr		Mon 5/11/15	Mon 5/11/15	Craig,Scott	2 hrs
15		0%	Monthly Status & Financial Reporting 8	1 hr		Wed 6/10/15	Wed 6/10/15	Craig,Scott	2 hrs
16		0%	Monthly Status & Financial Reporting 9	1 hr		Fri 7/10/15	Fri 7/10/15	Craig,Scott	2 hrs
17		0%	Monthly Status & Financial Reporting 10	1 hr		Mon 8/10/15	Mon 8/10/15	Craig,Scott	2 hrs
18		0%	Monthly Status & Financial Reporting 11	1 hr		Thu 9/10/15	Thu 9/10/15	Craig,Scott	2 hrs
19		17%	Ongoing Project Management	12 mons		Wed 10/1/14	Fri 9/11/15	Craig[2%]	30 hrs
20		17%	Ongoing Project Oversight	12 mons		Wed 10/1/14	Tue 9/8/15	Dr. Chute[10%]	192 hrs
21		52%	Execute	240 days	3	Fri 10/10/14	Fri 9/18/15		1,599.58 hrs
22		17%	Ongoing Operational Support	240 days	3	Fri 10/10/14	Fri 9/18/15		400 hrs
23		17%	Tech Support/Forum Management/Ongoing Technical Expertise	12 mons		Fri 10/10/14	Fri 9/18/15	Scott[25%]	400 hrs
24		0%	Milestone: Ongoing Operational Support Complete	0 days	22	Fri 9/18/15	Fri 9/18/15		0 hrs
25		96%	Maintenance and Support Development	105.79 days	3	Fri 10/10/14	Wed 3/11/15		1,025.58 hrs
26		100%	Supporting Item Development	6 days		Mon 10/20/14	Mon 10/20/14		20 hrs
28		100%	Milestone: Supporting Item Development Complete	0 days	26	Mon 10/20/14	Mon 10/20/14		0 hrs
29		10%	6.2 Deployment Tasks	5 days		Mon 1/12/15	Mon 1/19/15		30 hrs
30		10%	Deployment Tasks	5 days	44	Mon 1/12/15	Mon 1/19/15	Scott[75%]	30 hrs
31		99%	JIRA Item Development	105.79 days	3	Fri 10/10/14	Wed 3/11/15		975.58 hrs
32	LEXEVS-671	100%	SNOMEDCT does not load hierarchy or root nodes.	1 wk		Fri 10/10/14	Fri 10/17/14	Scott[75%]	30 hrs
33	LEXEVS-669	100%	Latest Version of SNOMEDCT Does not load transitivity table	2 wks	32	Fri 10/17/14	Fri 10/31/14	Scott[75%]	60 hrs
34	LEXEVS-667	100%	TreeService getTree method fails on remote call when the root node code appears in multiple namespaces.	2 wks	33	Fri 10/31/14	Fri 11/14/14	Scott[75%]	60 hrs
35	LEXEVS-598	100%	TreeService getTree method can fail when the root node code appears in multiple namespaces.	1 wk	34	Fri 11/14/14	Fri 11/21/14	Scott[75%]	30 hrs
36	LEXEVS-680	100%	Remove GEM loader documentation	1 hr	35	Fri 11/14/14	Fri 11/14/14	Scott[75%]	0.75 hrs
37		98%	OWL2 Development	80.67 days		Fri 11/14/14	Wed 3/11/15		681 hrs
38		100%	OWL2 Design Discussions	5 wks	36	Fri 11/14/14	Mon 12/22/14	Scott[75%]	150 hrs
39	LEXEVS-641	100%	OWL2 loader uses VersionIRI, but doesn't have a wide enough column	4 hrs	36	Fri 11/14/14	Fri 11/14/14	Scott[75%]	3 hrs
40	LEXEVS-614	100%	OWL2 associations and annotations on associations.	3.5 days	39	Fri 11/14/14	Thu 11/20/14	Scott[75%]	21 hrs
41	LEXEVS-684	100%	OWL2 Loader does not properly Parse output from render	10 days	40	Thu 11/20/14	Fri 12/5/14	Scott[75%]	60 hrs
42	LEXEVS-685	100%	OWL2 Loader loads disJointWith association as equivalent class	10 days	41	Fri 12/5/14	Fri 12/19/14	Scott[75%]	60 hrs
43	LEXEVS-583	100%	OWL2 data: restrictions on a class using datatype properties	6.67 days	42	Fri 12/19/14	Mon 1/5/15	Scott[75%]	40 hrs
44		100%	OWL Evaluation	2 wks	43	Mon 1/5/15	Mon 1/19/15	NCI Resource	80 hrs
45		100%	Revisit Tree Service	2.5 wks	44	Mon 1/19/15	Thu 2/5/15	Scott[75%]	75 hrs
46		100%	OWL2 Updates	6 wks	44FS+1 wk	Mon 1/26/15	Mon 3/9/15	Scott[75%]	180 hrs
47		0%	OWL2 Design Document	2 days	46	Mon 3/9/15	Wed 3/11/15	Scott[75%]	12 hrs
48	LEXEVS-623	100%	Mapping extension search methods fail on distributed mode.	9.67 days	36	Tue 12/23/14	Thu 1/8/15	Scott[75%],Kevin[25%]	53.33 hrs

S13-500 MOD4 LexEVS Project Plan

ID	JIRA#	% Complete	Task Name	Duration	Predecessors	Start	Finish	Resource Names	Work	Sep
49	LEXEVS-679	100%	Expand loader documentation to include creating, running, and errors information.	2.67 days	44	Mon 1/12/15	Thu 1/15/15	Scott[75%]	16 hrs	
50	LEXEVSCTS2-8	100%	UI - Only 50 entries are returned for value sets that have more than 50 entries	1 hr	27FS+4 wks	Mon 11/17/14	Mon 11/17/14	Cory[50%]	0.5 hrs	
51	LEXEVSCTS2-21	100%	Value Set resolution fails when a value set name is more than a particular number of characters.	3 days	50	Mon 11/17/14	Wed 12/10/14	Cory[50%]	12 hrs	
52	LEXEVSCTS2-27	100%	Create interactive CTS2 API documentation	1 wk	51	Wed 12/10/14	Wed 12/17/14	Cory[50%]	20 hrs	
53	LEXEVS-636	100%	LexEVSValueSetDefinitionServices exportValueSetResolution method returns unprocessable InputStream.	0.8 wks		Fri 1/16/15	Thu 1/22/15	Kevin[25%]	8 hrs	
54	LEXEVSCTS2-28	100%	NLM (VSAC) CTS2 Service authentication is failing	2 days	43	Mon 1/5/15	Wed 1/7/15	Kevin[25%]	4 hrs	
55		0%	Milestone: JIRA Item Development Complete	0 days	31	Wed 3/11/15	Wed 3/11/15		0 hrs	
56		0%	Milestone - Maintenance and Support Development Complete	0 days	25	Wed 3/11/15	Wed 3/11/15		0 hrs	
57		100%	Next Release Planning	10 days		Mon 1/19/15	Mon 2/2/15		100 hrs	
58		100%	Agile Configuration and Project Planning	2 wks	44	Mon 1/19/15	Mon 2/2/15	Cory[25%],Craig	100 hrs	
59		100%	Update Technical Documentation	7 days		Mon 1/26/15	Wed 2/4/15		14 hrs	
60		100%	Deploy CTS2 API Documentation Service (External)	2 days	44FS+1 wk	Mon 1/26/15	Wed 1/28/15	Cory[25%]	4 hrs	
61		100%	Documentation Structure	1 day	60	Wed 1/28/15	Thu 1/29/15	Cory[25%]	2 hrs	
62		100%	Design and Architecture Guide	1 day	61	Thu 1/29/15	Fri 1/30/15	Cory[25%]	2 hrs	
63		100%	Programmer's Guide	1 day	62	Fri 1/30/15	Mon 2/2/15	Cory[25%]	2 hrs	
64		100%	Install Guide	1 day	63	Mon 2/2/15	Tue 2/3/15	Cory[25%]	2 hrs	
65		100%	Administrator Guide	1 day	64	Tue 2/3/15	Wed 2/4/15	Cory[25%]	2 hrs	
66		0%	Milestone: Update Technical Documentation Complete	0 days	59	Wed 2/4/15	Wed 2/4/15		0 hrs	
67		0%	Tier Deployment at NCI	6 days		Wed 3/11/15	Thu 3/19/15		60 hrs	
68		0%	Dev Deployment	6 days	25	Wed 3/11/15	Thu 3/19/15		60 hrs	
69		0%	Deploy Updated LexEVS 6.3	2 days		Wed 3/11/15	Fri 3/13/15	Scott[75%],Cory[50%]	20 hrs	
70		0%	Deploy Updated LexEVS 6.3 CTS2 Service	2 days	69	Fri 3/13/15	Tue 3/17/15	Scott[75%],Cory[50%]	20 hrs	
71		0%	Deploy Updated LexEVS 6.3 URI Resolver Service	2 days	70	Tue 3/17/15	Thu 3/19/15	Scott[75%],Cory[50%]	20 hrs	
72		0%	Milestone: Tier Deployment at NCI	0 days	67	Thu 3/19/15	Thu 3/19/15		0 hrs	
73		0%	Milestone: S13-500 MOD4 LexEVS Project Plan Complete	0 days	67	Thu 3/19/15	Thu 3/19/15		0 hrs	

S13-500 MOD4 LexEVS Project Plan

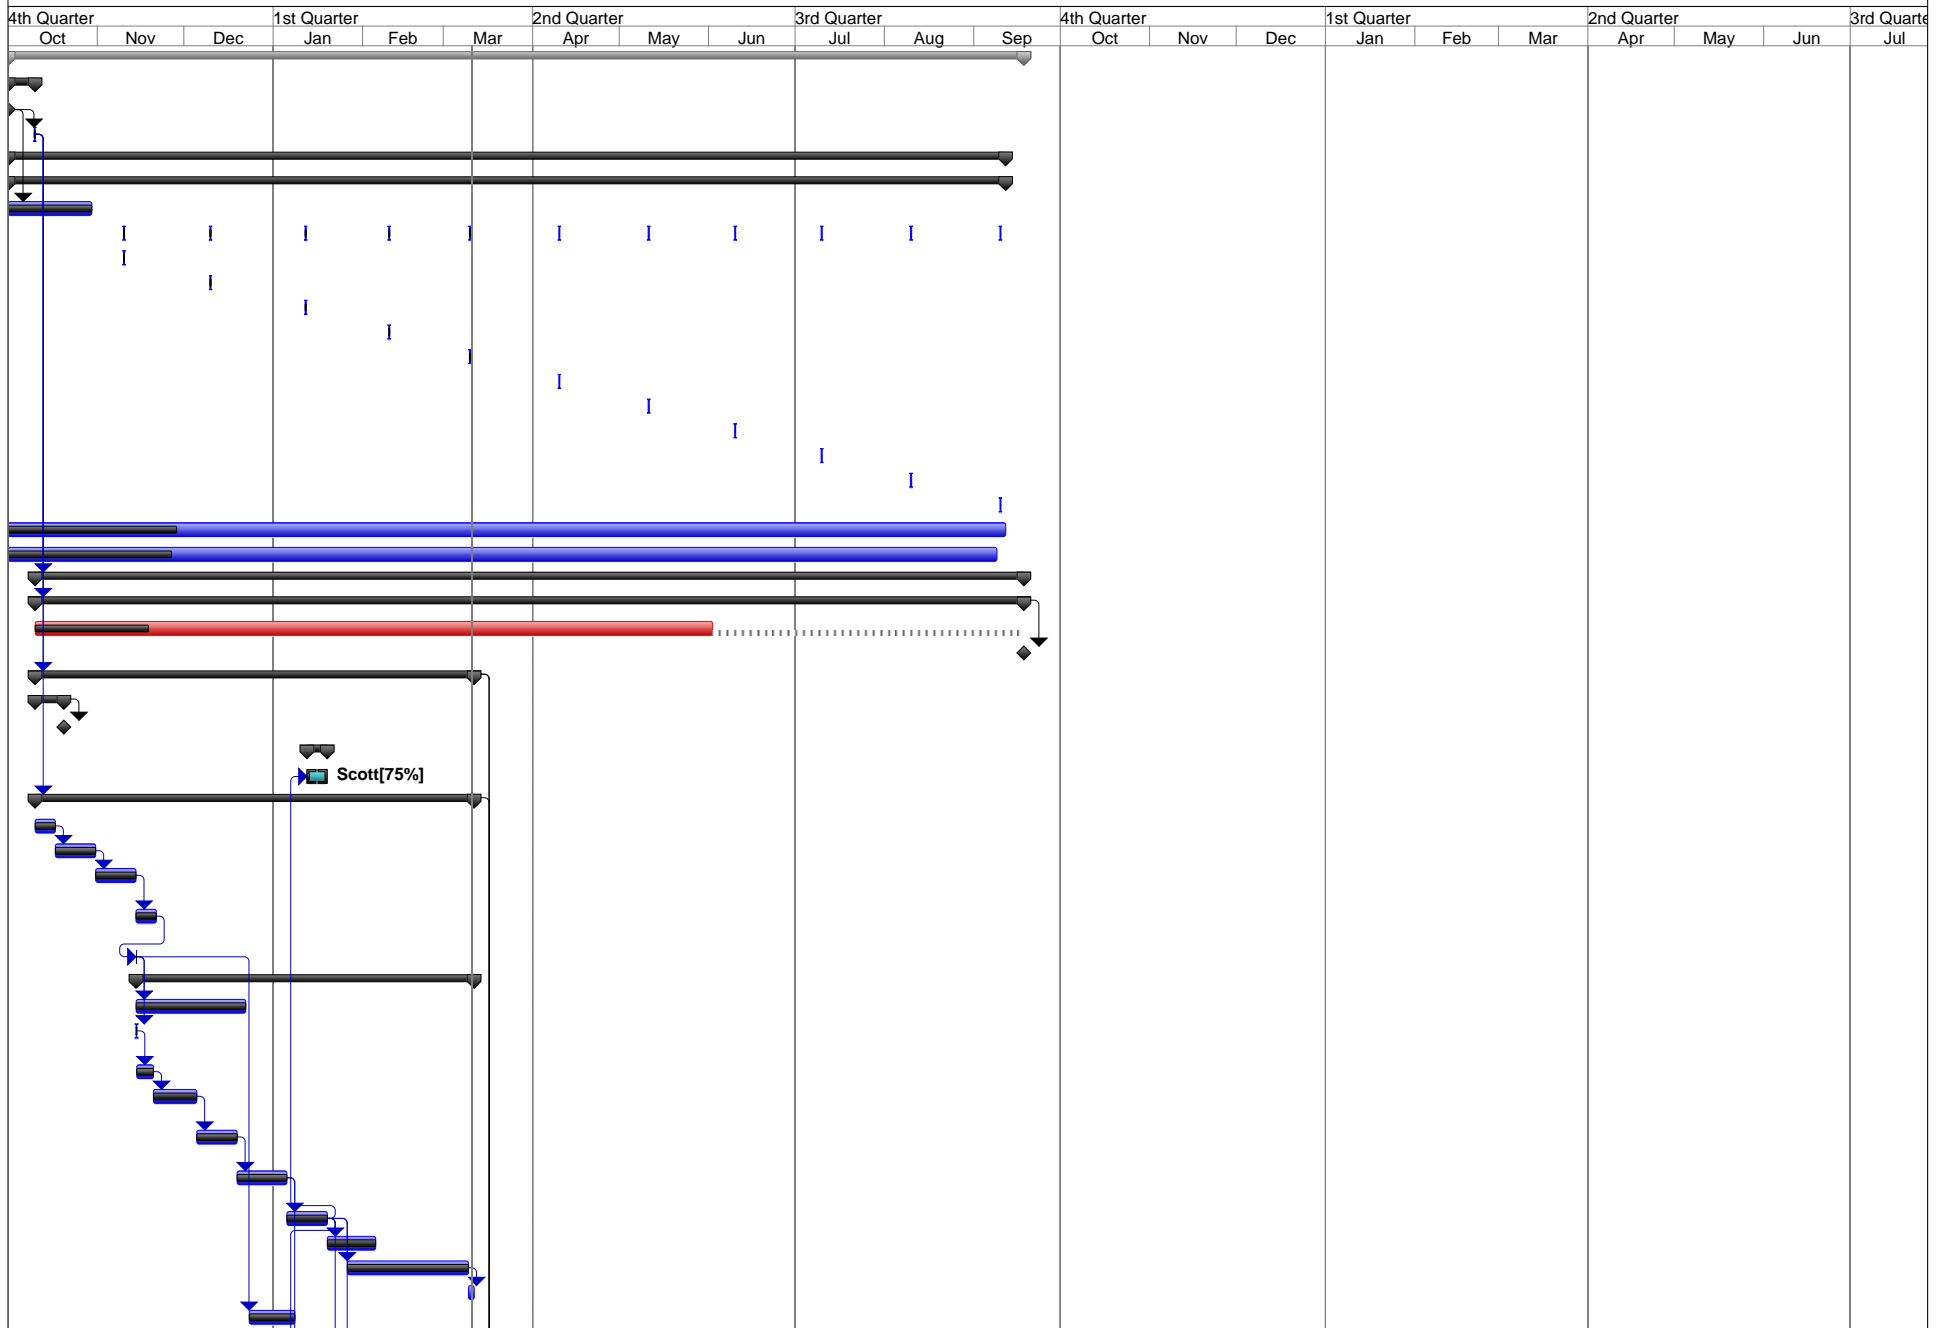

S13-500 MOD4 LexEVS Project Plan

