


S13-500 MOD4 LexEVS Lucene Project Roadmap

ID	JIRA#	% Complete	Task Name	Duration	Predecessor	Start
0		63%	S13-500 MOD4 LexEVS Lucene Project Roadmap	285 days		Mon 3/9/15
1		63%	Execute	285 days		Mon 3/9/15
2		63%	Technical Development	285 days		Mon 3/9/15
3	LEXEVS-849	62%	Provide support to the existing LexEVS project	8 mons		Mon 3/9/15
4		100%	6.4 - Phase -Planning	10 days		Mon 3/9/15
5	LEXEVS-692	100%	Project planning and estimates	10 days		Mon 3/9/15
6		100%	6.4 - Phase - Architecture and Design	35 days		Wed 3/25/15
7	LEXEVS-722	100%	Document project design and architecture	35 days		Wed 3/25/15
8		100%	Sprint 2	2 wks	4FS+2 days	Wed 3/25/15
9		100%	Sprint 3	2 wks	8	Wed 4/8/15
10		100%	Sprint 4 (6.3 focus)	3 wks	9	Wed 4/22/15
11		100%	6.4 - Phase - Phase 1	40 days		Wed 5/13/15
12	LEXEVS-693	100%	Demonstrate viability of the new Lucene approach and update of all dependencies.	40 days	6	Wed 5/13/15
13		100%	Sprint 5	3 wks		Wed 5/13/15
14		100%	Sprint 6	3 wks	13	Thu 6/4/15
15		100%	Sprint 7	2 wks	14	Thu 6/25/15
16		100%	6.4 - Phase - Phase 2	20 days		Thu 7/9/15
17	LEXEVS-694	100%	All internal interfaces and code structure in place and documented	20 days	11	Thu 7/9/15
18		100%	Sprint 8	2 wks		Thu 7/9/15
19		100%	Sprint 9	2 wks	18	Thu 7/23/15
20		100%	6.4 - Phase - Phase 3	39 days		Thu 8/6/15
21	LEXEVS-695	100%	Demonstrate functionality of any search being performed in the GUI and 25% of unit tests pass and documented	39 days	16	Thu 8/6/15
22		100%	Sprint 10	2 wks	19	Thu 8/6/15
23		100%	Sprint 11	2 wks	22	Thu 8/20/15
24		100%	Sprint 12	9 days	23	Thu 9/3/15
25		100%	Sprint 13	2 wks	24	Thu 9/17/15
26		88%	6.4 - Phase - Phase 4 (60 days)	39 days		Thu 10/1/15
27	LEXEVS-696	88%	Demonstrate all previous LexEVS functionality as implemented with the new Lucene and 100% of unit test pass	39 days	20	Thu 10/1/15
28		100%	Sprint 14	2 wks		Thu 10/1/15
29		100%	Sprint 15	2 wks	28	Thu 10/15/15
30		100%	Sprint 16	2 wks	29	Thu 10/29/15
31		50%	Sprint 17	9 days	30	Thu 11/12/15
32		0%	6.4 - Phase - Phase 5	30 days		Wed 11/25/15
33	LEXEVS-697	0%	Demonstrate complete LexEVS functionality including remote API and CTS2 services	30 days	26	Wed 11/25/15
34		0%	6.4 - Phase - Documentation	10 days		Wed 1/6/16
35	LEXEVS-725	0%	Provide documentation for the product release	10 days	32	Wed 1/6/16
36		0%	6.4 - Phase - Tier Deployment	60 days		Wed 1/20/16

S13-500 MOD4 LexEVS Lucene Project Roadmap

ID	JIRA#	% Complete	Task Name	Duration	Predecessor	Start
37	LEXEVS-728	0%	Demonstrate complete LexEVS functionality running on NCI production.	60 days	34	Wed 1/20/16
38		0%	Milestone - Technical Development Complete	0 days	2	Tue 4/12/16
39		0%	Milestone: S13-500 MOD4 LexEVS Lucene Project Roadmap Complete	0 days	1	Tue 4/12/16

S13-500 MOD4 LexEVS Lucene Project Roadmap

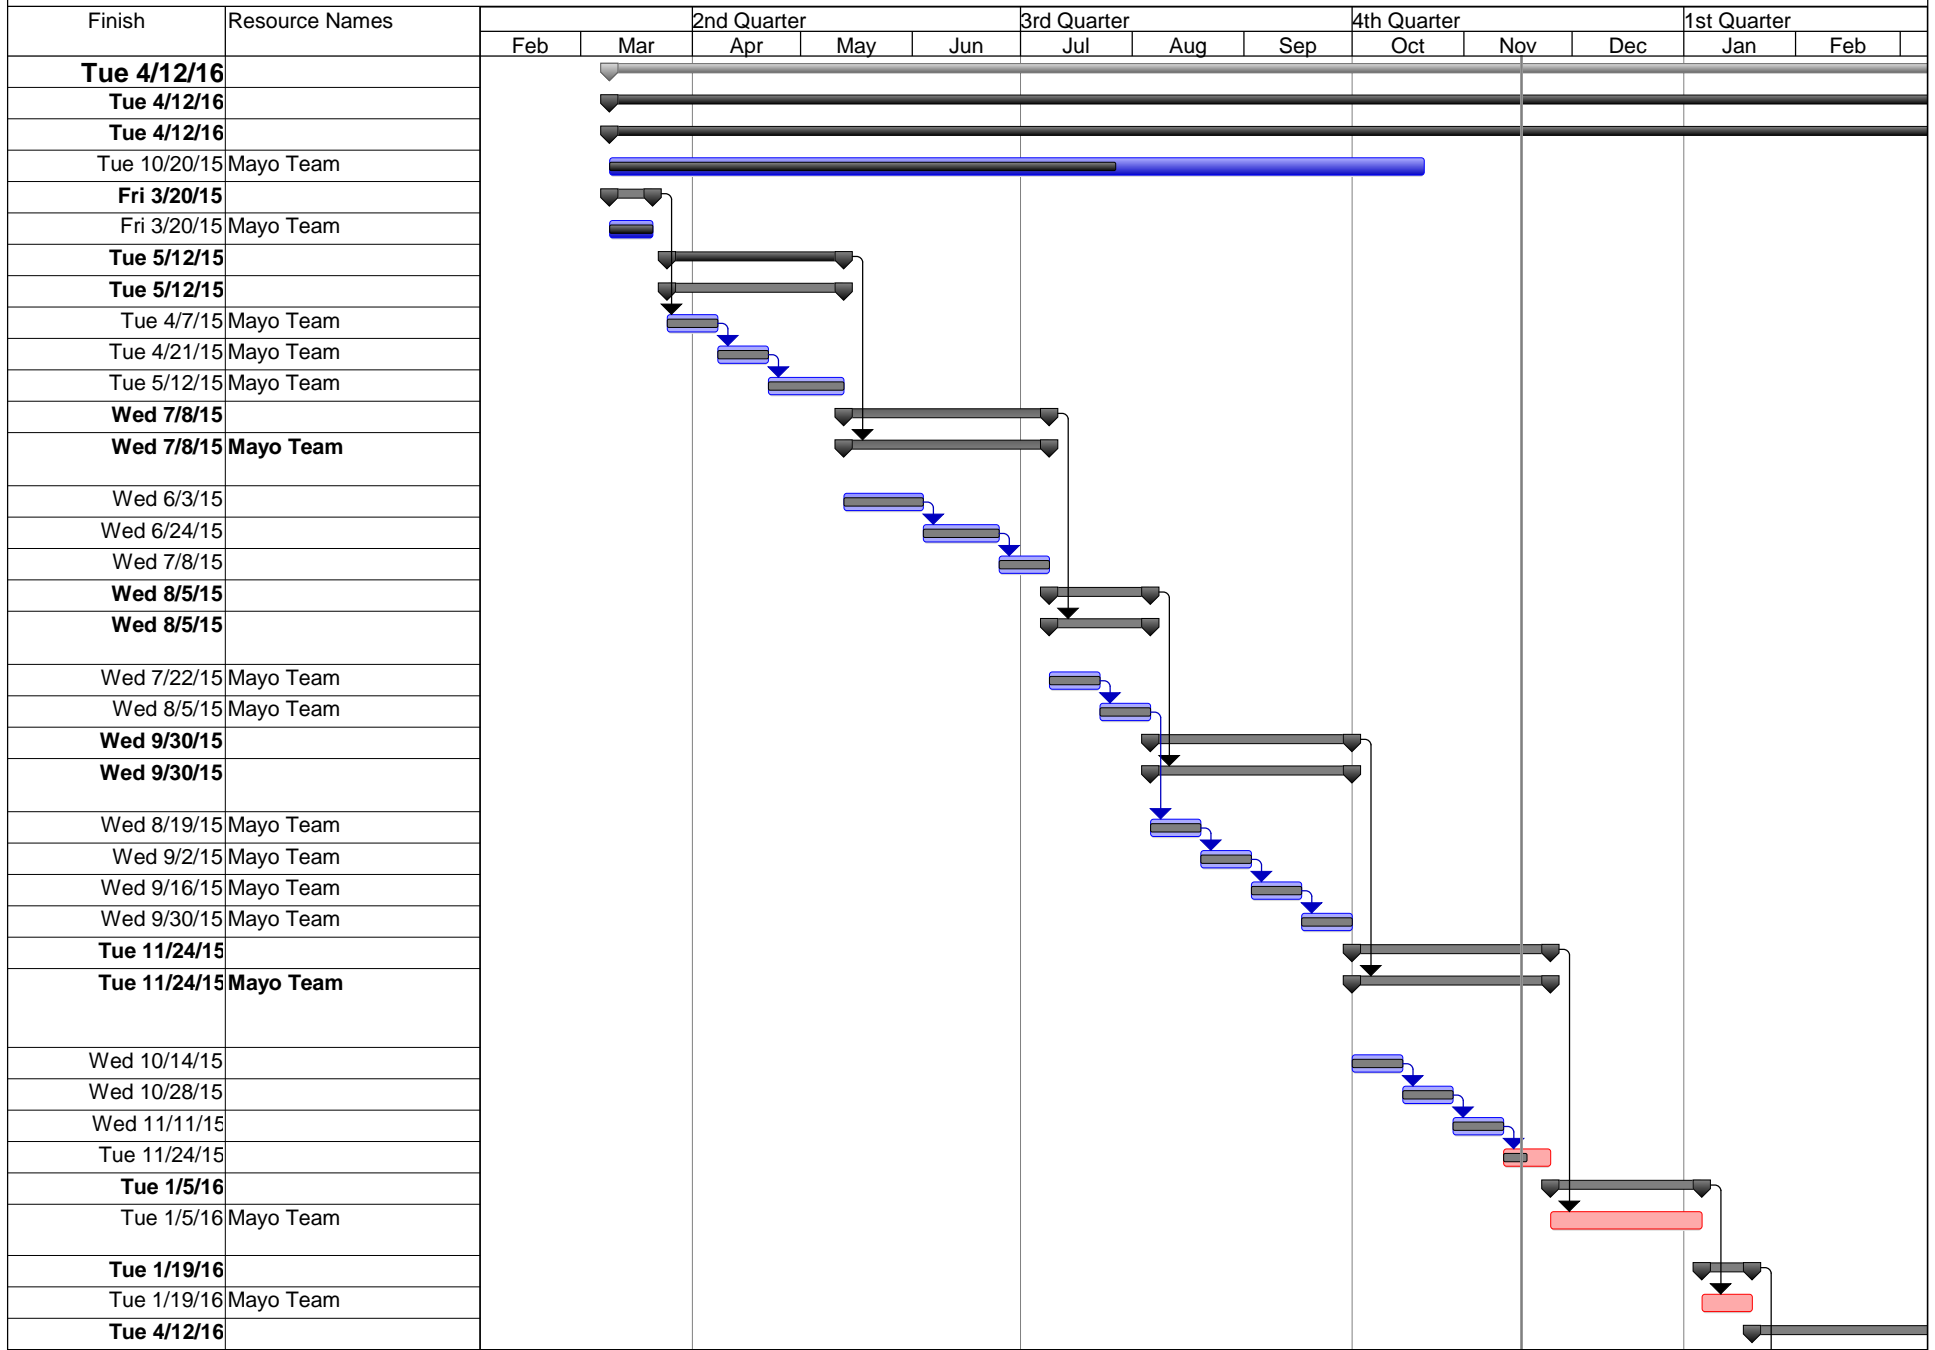

S13-500 MOD4 LexEVS Lucene Project Roadmap

Finish	Resource Names	2nd Quarter			3rd Quarter			4th Quarter			1st Quarter			
		Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb
Tue 4/12/16	Mayo Team													
Tue 4/12/16														
Tue 4/12/16														

S13-500 MOD4 LexEVS Lucene Project Roadmap

2nd Quarter				3rd Quarter			4th Quarter			1st Quarter			2nd Quarter			3rd Quarter	
Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	A
