
































S13-500 MOD4 LexEVS Lucene Project Roadmap

ID		JIRA#	% Complete	Task Name	Duration	Predecessor	Start
0			<b>64%</b>	<b>S13-500 MOD4 LexEVS Lucene Project Roadmap</b>	<b>306 days</b>		<b>Mon 3/9/15</b>
1			<b>64%</b>	<b>Execute</b>	<b>306 days</b>		<b>Mon 3/9/15</b>
2			<b>64%</b>	<b>Technical Development</b>	<b>306 days</b>		<b>Mon 3/9/15</b>
3		LEXEVS-849	62%	Provide support to the existing LexEVS project	8 mons		Mon 3/9/15
4			<b>100%</b>	<b>6.4 - Phase -Planning</b>	<b>10 days</b>		<b>Mon 3/9/15</b>
5		LEXEVS-692	100%	Project planning and estimates	10 days		Mon 3/9/15
6			<b>100%</b>	<b>6.4 - Phase - Architecture and Design</b>	<b>35 days</b>		<b>Wed 3/25/15</b>
7		<b>LEXEVS-722</b>	<b>100%</b>	<b>Document project design and architecture</b>	<b>35 days</b>		<b>Wed 3/25/15</b>
8			100%	Sprint 2	2 wks	4FS+2 days	Wed 3/25/15
9			100%	Sprint 3	2 wks	8	Wed 4/8/15
10			100%	Sprint 4 (6.3 focus)	3 wks	9	Wed 4/22/15
11			<b>100%</b>	<b>6.4 - Phase - Phase 1</b>	<b>40 days</b>		<b>Wed 5/13/15</b>
12		<b>LEXEVS-693</b>	<b>100%</b>	<b>Demonstrate viability of the new Lucene approach and update of all dependencies.</b>	<b>40 days</b>	<b>6</b>	<b>Wed 5/13/15</b>
13			100%	Sprint 5	3 wks		Wed 5/13/15
14			100%	Sprint 6	3 wks	13	Thu 6/4/15
15			100%	Sprint 7	2 wks	14	Thu 6/25/15
16			<b>100%</b>	<b>6.4 - Phase - Phase 2</b>	<b>20 days</b>		<b>Thu 7/9/15</b>
17		<b>LEXEVS-694</b>	<b>100%</b>	<b>All internal interfaces and code structure in place and documented</b>	<b>20 days</b>	<b>11</b>	<b>Thu 7/9/15</b>
18			100%	Sprint 8	2 wks		Thu 7/9/15
19			100%	Sprint 9	2 wks	18	Thu 7/23/15
20			<b>100%</b>	<b>6.4 - Phase - Phase 3</b>	<b>39 days</b>		<b>Thu 8/6/15</b>
21		<b>LEXEVS-695</b>	<b>100%</b>	<b>Demonstrate functionality of any search being performed in the GUI and 25% of unit tests pass and documented</b>	<b>39 days</b>	<b>16</b>	<b>Thu 8/6/15</b>
22			100%	Sprint 10	2 wks	19	Thu 8/6/15
23			100%	Sprint 11	2 wks	22	Thu 8/20/15
24			100%	Sprint 12	9 days	23	Thu 9/3/15
25			100%	Sprint 13	2 wks	24	Thu 9/17/15
26			<b>92%</b>	<b>6.4 - Phase - Phase 4 (60 days)</b>	<b>60 days</b>		<b>Thu 10/1/15</b>
27		<b>LEXEVS-696</b>	<b>92%</b>	<b>Demonstrate all previous LexEVS functionality as implemented with the new Lucene and 100% of unit test pass</b>	<b>60 days</b>	<b>20</b>	<b>Thu 10/1/15</b>
28			100%	Sprint 14	2 wks		Thu 10/1/15
29			100%	Sprint 15	2 wks	28	Thu 10/15/15
30			100%	Sprint 16	2 wks	29	Thu 10/29/15
31			100%	Sprint 17	9 days	30	Thu 11/12/15
32			100%	Sprint 18	2 wks	31	Thu 11/26/15
33			50%	Sprint 19	2 wks	32	Thu 12/10/15
34			<b>0%</b>	<b>6.4 - Phase - Phase 5</b>	<b>30 days</b>		<b>Thu 12/24/15</b>
35		LEXEVS-697	0%	Demonstrate complete LexEVS functionality including remote API and CTS2 services	30 days	26	Thu 12/24/15
36			<b>0%</b>	<b>6.4 - Phase - Documentation</b>	<b>10 days</b>		<b>Thu 2/4/16</b>

S13-500 MOD4 LexEVS Lucene Project Roadmap


ID	JIRA#	% Complete	Task Name	Duration	Predecessor	Start
37	LEXEVS-725	0%	Provide documentation for the product release	10 days	34	Thu 2/4/16
38		<b>0%</b>	<b>6.4 - Phase - Tier Deployment</b>	<b>60 days</b>		<b>Thu 2/18/16</b>
39	LEXEVS-728	0%	Demonstrate complete LexEVS functionality running on NCI production.	60 days	36	Thu 2/18/16
40		0%	<b>Milestone - Technical Development Complete</b>	0 days	2	Wed 5/11/16
41		0%	<b>Milestone: S13-500 MOD4 LexEVS Lucene Project Roadmap Complete</b>	0 days	1	Wed 5/11/16

S13-500 MOD4 LexEVS Lucene Project Roadmap

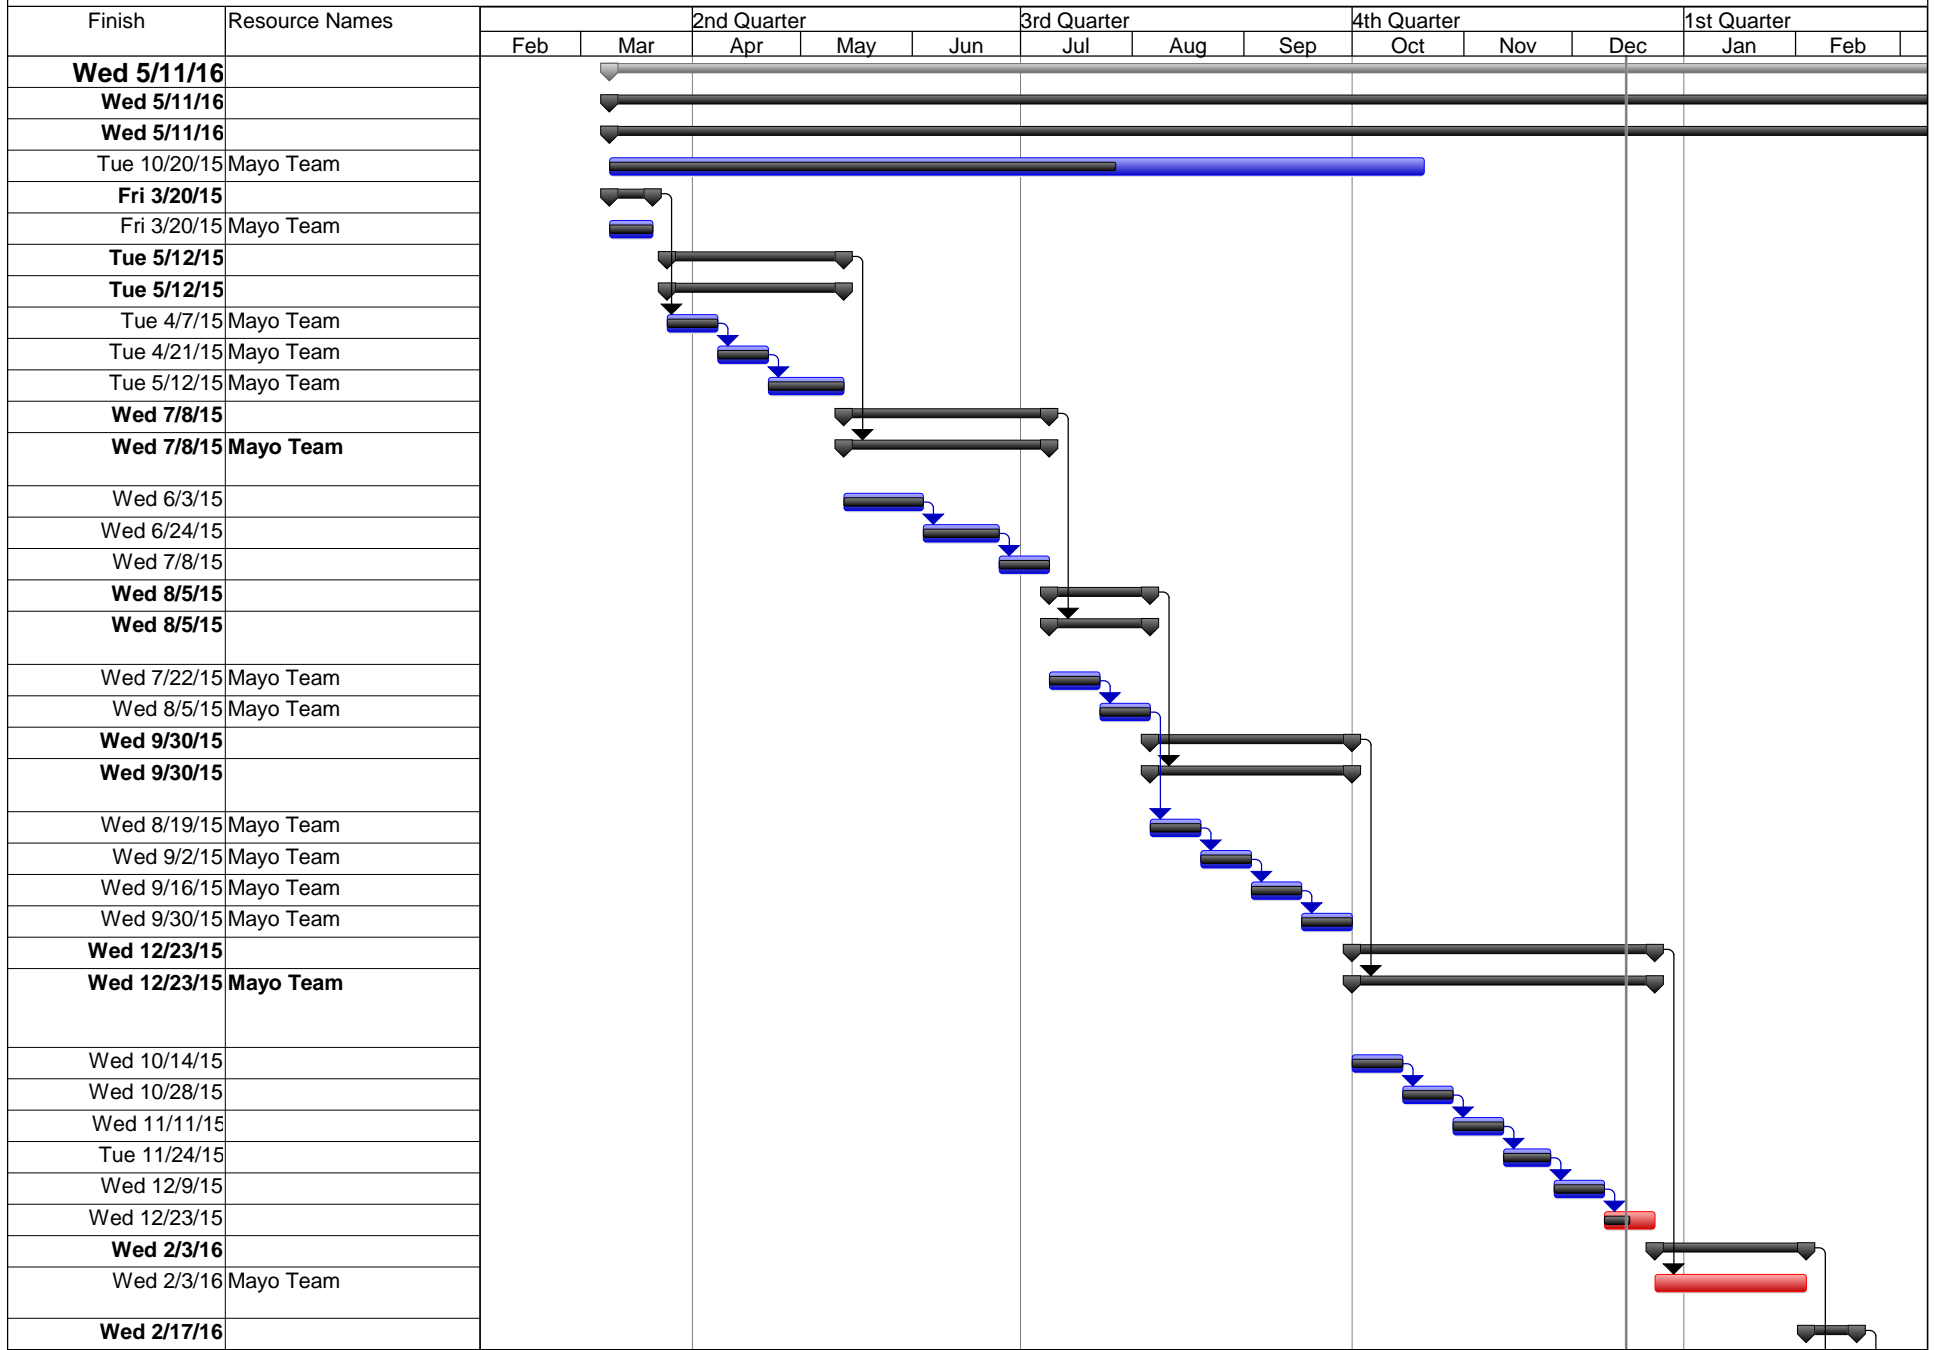

S13-500 MOD4 LexEVS Lucene Project Roadmap

Finish	Resource Names	2nd Quarter					3rd Quarter			4th Quarter			1st Quarter					
		Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb				
Wed 2/17/16	Mayo Team																	
<b>Wed 5/11/16</b>																		
Wed 5/11/16	Mayo Team																	
Wed 5/11/16																		
Wed 5/11/16																		





S13-500 MOD4 LexEVS Lucene Project Roadmap

2nd Quarter			3rd Quarter			4th Quarter			1st Quarter			2nd Quarter			3rd Quarter		
Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	A
