


S13-500 MOD4 LexEVS Lucene Project Roadmap

ID	JIRA#	% Complete	Task Name	Duration	Predecessor	Start
0		<b>63%</b>	<b>S13-500 MOD4 LexEVS Lucene Project Roadmap</b>	<b>346 days</b>		<b>Mon 3/9/15</b>
1		<b>63%</b>	<b>Execute</b>	<b>346 days</b>		<b>Mon 3/9/15</b>
2		<b>63%</b>	<b>Technical Development</b>	<b>346 days</b>		<b>Mon 3/9/15</b>
3	LEXEVS-849	62%	Provide support to the existing LexEVS project	8 mons		Mon 3/9/15
4		<b>100%</b>	<b>6.4 - Phase -Planning</b>	<b>10 days</b>		<b>Mon 3/9/15</b>
6		<b>100%</b>	<b>6.4 - Phase - Architecture and Design</b>	<b>35 days</b>		<b>Wed 3/25/15</b>
11		<b>100%</b>	<b>6.4 - Phase - Phase 1</b>	<b>40 days</b>		<b>Wed 5/13/15</b>
16		<b>100%</b>	<b>6.4 - Phase - Phase 2</b>	<b>20 days</b>		<b>Thu 7/9/15</b>
20		<b>100%</b>	<b>6.4 - Phase - Phase 3</b>	<b>39 days</b>		<b>Thu 8/6/15</b>
26		<b>75%</b>	<b>6.4 - Phase - Phase 4 (60 days)</b>	<b>100 days</b>		<b>Thu 10/1/15</b>
27	LEXEVS-696	<b>75%</b>	<b>Demonstrate all previous LexEVS functionality as implemented with the new Lucene and 100% of unit test pass</b>	<b>100 days</b>	<b>20</b>	<b>Thu 10/1/15</b>
28		100%	Sprint 14	2 wks		Thu 10/1/15
29		100%	Sprint 15	2 wks	28	Thu 10/15/15
30		100%	Sprint 16	2 wks	29	Thu 10/29/15
31		100%	Sprint 17	9 days	30	Thu 11/12/15
32		100%	Sprint 18	2 wks	31	Thu 11/26/15
33		100%	Sprint 19	2 wks	32	Thu 12/10/15
34		100%	Sprint 20	2 wks	33	Thu 12/24/15
35		50%	Sprint 21	2 wks	34	Thu 1/7/16
36		0%	Sprint 22	2 wks	35	Thu 1/21/16
37		0%	Sprint 23	2 wks	36	Thu 2/4/16
38		<b>0%</b>	<b>6.4 - Phase - Phase 5</b>	<b>30 days</b>		<b>Thu 2/18/16</b>
39	LEXEVS-697	0%	Demonstrate complete LexEVS functionality including remote API and CTS2 services	30 days	26	Thu 2/18/16
40		0%	<b>Milestone - Functionality Complete</b>	0 days	16,20,26,38	Wed 3/30/16
41		<b>0%</b>	<b>6.4 - Phase - Documentation</b>	<b>10 days</b>		<b>Thu 3/31/16</b>
42	LEXEVS-725	0%	Provide documentation for the product release	10 days	38	Thu 3/31/16
43		<b>0%</b>	<b>6.4 - Phase - Tier Deployment</b>	<b>60 days</b>		<b>Thu 4/14/16</b>
44	LEXEVS-728	0%	Demonstrate complete LexEVS functionality running on NCI production.	60 days	41	Thu 4/14/16
45		0%	<b>Milestone - Technical Development Complete</b>	0 days	2	Wed 7/6/16
46		0%	<b>Milestone: S13-500 MOD4 LexEVS Lucene Project Roadmap Complete</b>	0 days	1	Wed 7/6/16

S13-500 MOD4 LexEVS Lucene Project Roadmap

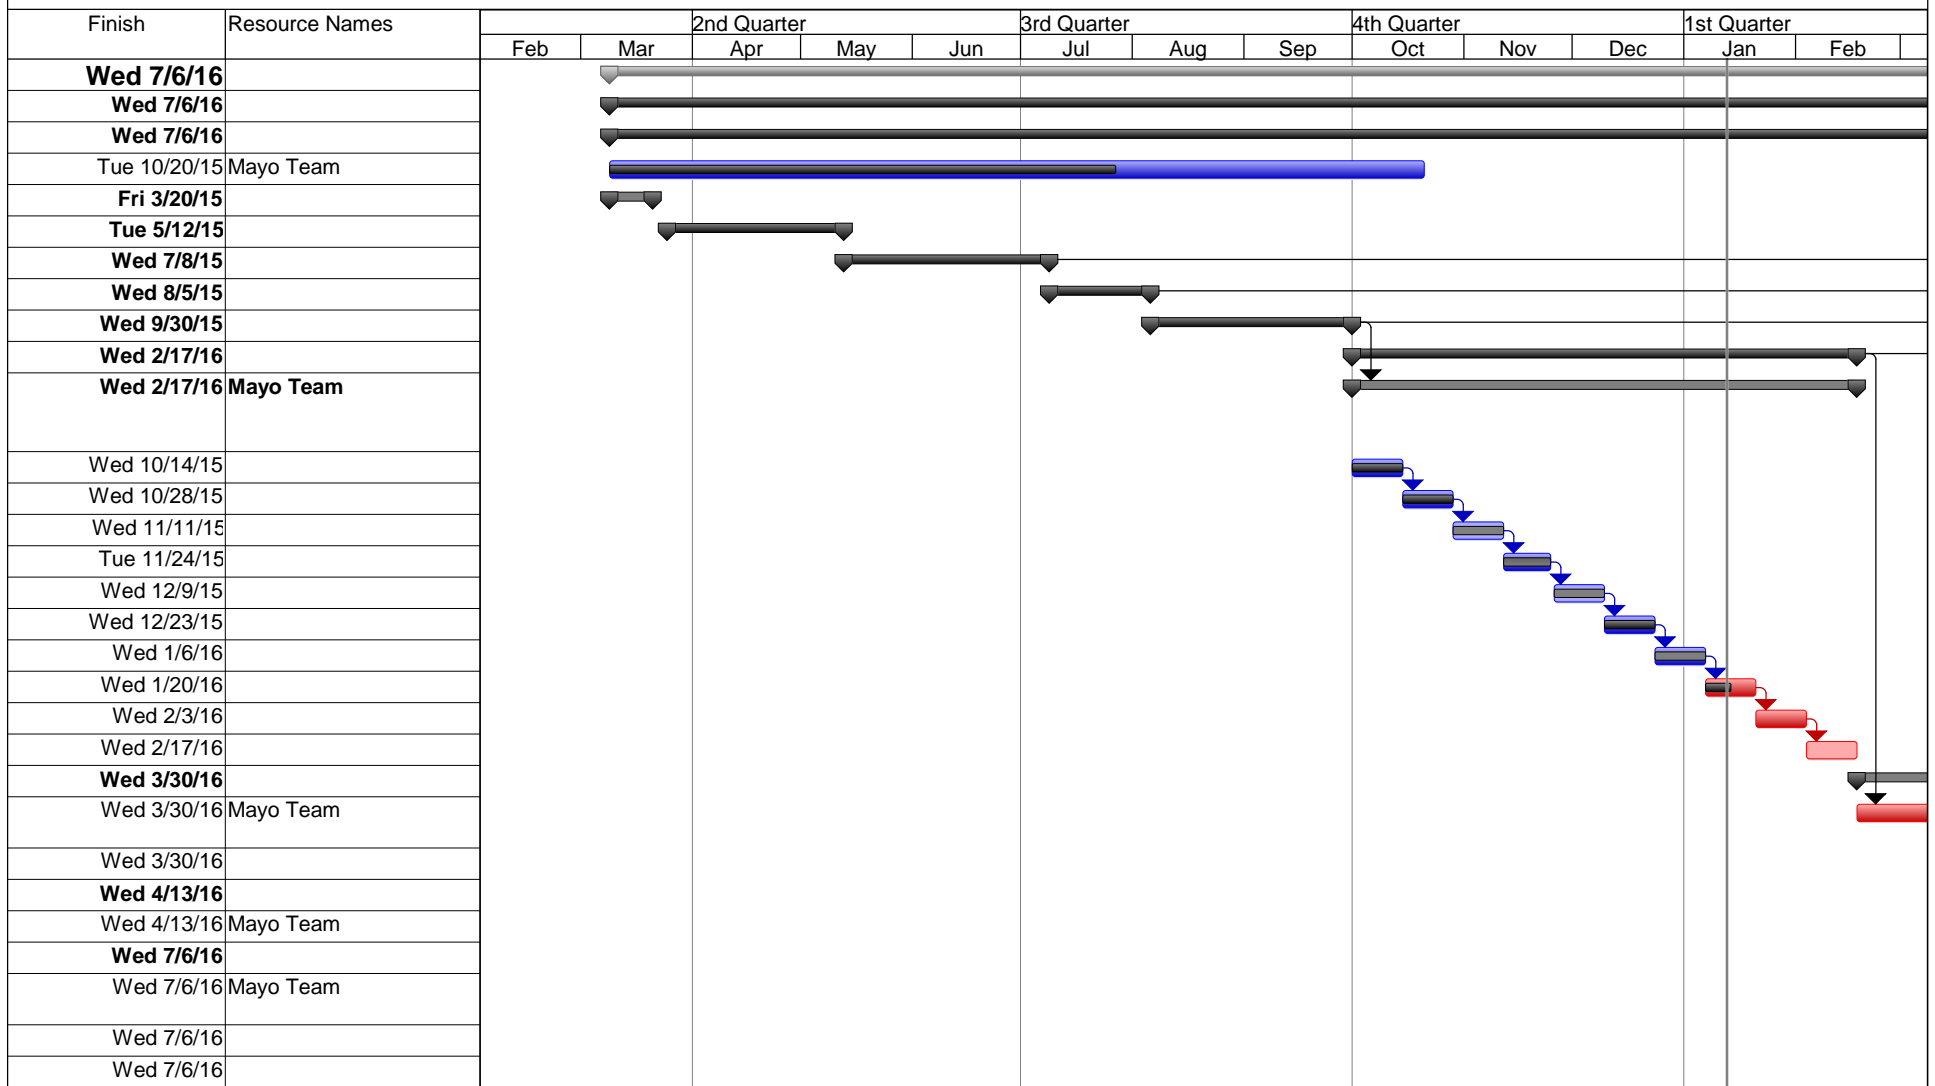

S13-500 MOD4 LexEVS Lucene Project Roadmap

