


S13-500 MOD4 LexEVS Lucene Project Roadmap

ID	JIRA#	% Complete	Task Name	Duration	Predecessor	Start
0		89%	S13-500 MOD4 LexEVS Lucene Project Roadmap	405.5 days		Mon 3/9/15
1		89%	Execute	405.5 days		Mon 3/9/15
2		89%	Technical Development	366 days		Mon 3/9/15
3	LEXEVS-849	62%	Provide support to the existing LexEVS project	8 mons		Mon 3/9/15
4		100%	6.4 - Phase -Planning	10 days		Mon 3/9/15
6		100%	6.4 - Phase - Architecture and Design	35 days		Wed 3/25/15
11		100%	6.4 - Phase - Phase 1	40 days		Wed 5/13/15
16		100%	6.4 - Phase - Phase 2	20 days		Thu 7/9/15
20		100%	6.4 - Phase - Phase 3	39 days		Thu 8/6/15
26		100%	6.4 - Phase - Phase 4 (60 days)	110 days		Thu 10/1/15
39		99%	6.4 - Phase - Phase 5	60 days		Thu 3/3/16
47		100%	Milestone - Functionality Complete	0 days	16,20,26,39	Wed 5/25/16
48		100%	6.4 - Phase - Documentation (10 Days)	10 days		Thu 5/26/16
50		100%	6.4 - Phase - Tier Deployment (60 Days)	50 days		Thu 5/26/16
57		88%	LexEVS Development	405.5 days		Mon 3/9/15
58		100%	Sprint 36	2 wks	56	Thu 8/4/16
59		100%	Sprint 37	2 wks	58	Mon 3/9/15
60		100%	Sprint 38	2 wks	59	Wed 8/31/16
61		50%	Sprint 39	2 wks	60	Wed 9/14/16
62		0%	Milestone - Technical Development Complete	0 days	2	Wed 8/3/16
63		0%	Milestone: S13-500 MOD4 LexEVS Lucene Project Roadmap Complete	0 days	1	Wed 9/28/16

S13-500 MOD4 LexEVS Lucene Project Roadmap

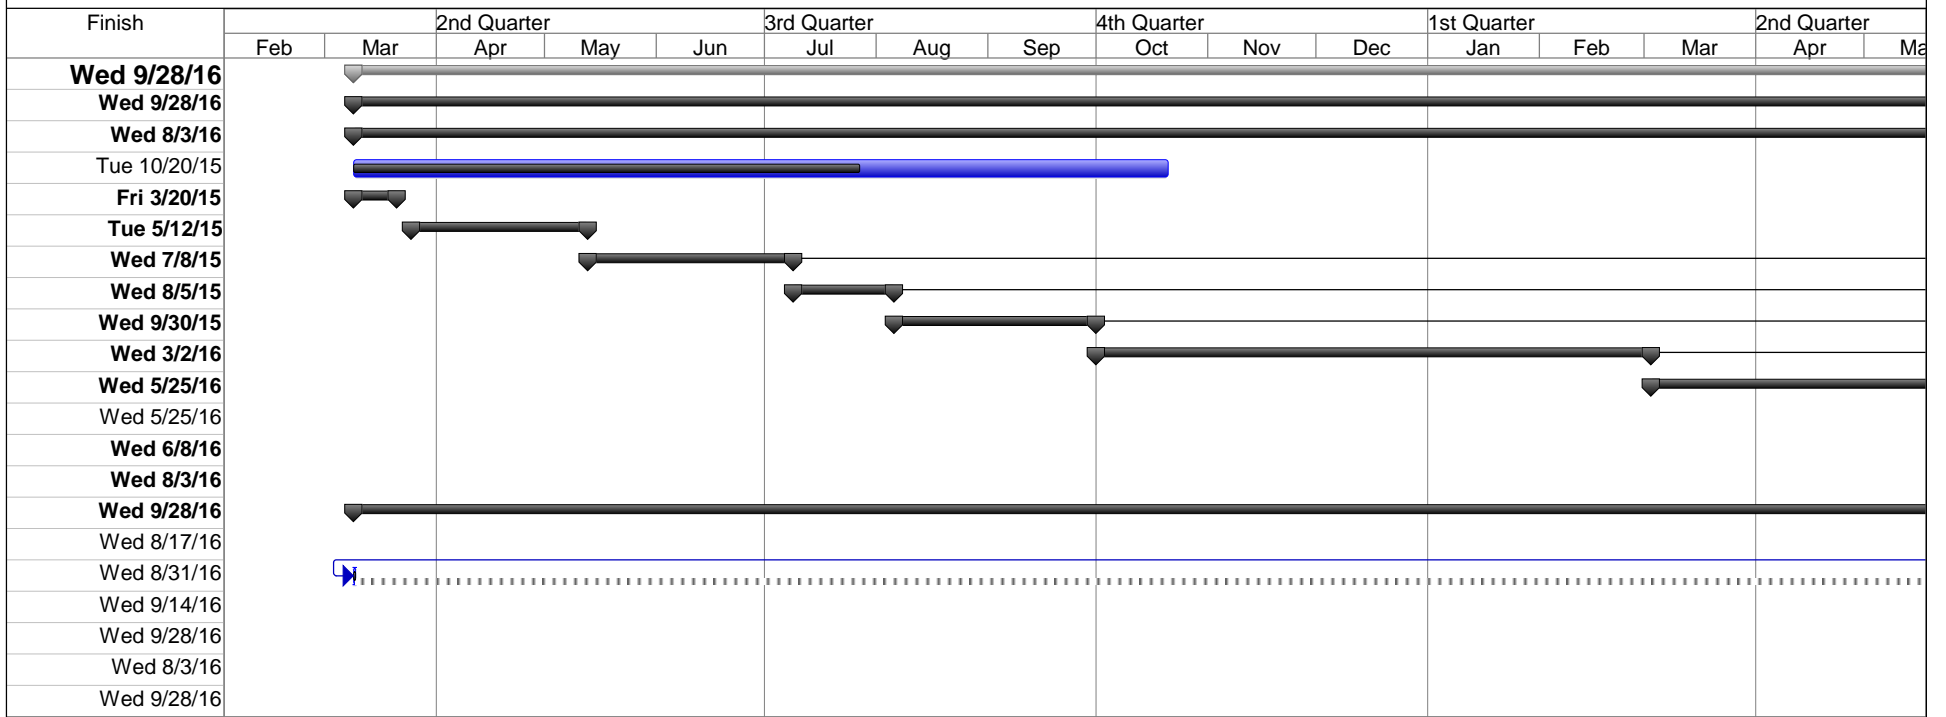

S13-500 MOD4 LexEVS Lucene Project Roadmap

