


S13-500 MOD4 LexEVS Lucene Project Roadmap

ID	JIRA#	% Complete	Task Name	Duration	Predecessor	Start
0		<b>88%</b>	<b>S13-500 MOD4 LexEVS Lucene Project Roadmap</b>	<b>405.5 days</b>		<b>Mon 3/9/15</b>
1		<b>88%</b>	<b>Execute</b>	<b>405.5 days</b>		<b>Mon 3/9/15</b>
2		<b>89%</b>	<b>Technical Development</b>	<b>366 days</b>		<b>Mon 3/9/15</b>
3	LEXEVS-849	62%	Provide support to the existing LexEVS project	8 mons		Mon 3/9/15
4		<b>100%</b>	<b>6.4 - Phase -Planning</b>	<b>10 days</b>		<b>Mon 3/9/15</b>
6		<b>100%</b>	<b>6.4 - Phase - Architecture and Design</b>	<b>35 days</b>		<b>Wed 3/25/15</b>
11		<b>100%</b>	<b>6.4 - Phase - Phase 1</b>	<b>40 days</b>		<b>Wed 5/13/15</b>
16		<b>100%</b>	<b>6.4 - Phase - Phase 2</b>	<b>20 days</b>		<b>Thu 7/9/15</b>
20		<b>100%</b>	<b>6.4 - Phase - Phase 3</b>	<b>39 days</b>		<b>Thu 8/6/15</b>
26		<b>100%</b>	<b>6.4 - Phase - Phase 4 (60 days)</b>	<b>110 days</b>		<b>Thu 10/1/15</b>
39		<b>99%</b>	<b>6.4 - Phase - Phase 5</b>	<b>60 days</b>		<b>Thu 3/3/16</b>
47		100%	<b>Milestone - Functionality Complete</b>	0 days	16,20,26,39	Wed 5/25/16
48		<b>100%</b>	<b>6.4 - Phase - Documentation (10 Days)</b>	<b>10 days</b>		<b>Thu 5/26/16</b>
50		<b>100%</b>	<b>6.4 - Phase - Tier Deployment (60 Days)</b>	<b>50 days</b>		<b>Thu 5/26/16</b>
57		<b>75%</b>	<b>LexEVS Development</b>	<b>405.5 days</b>		<b>Mon 3/9/15</b>
58		100%	Sprint 36	2 wks	56	Thu 8/4/16
59		100%	Sprint 37	2 wks	58	Mon 3/9/15
60		100%	Sprint 38	2 wks	59	Wed 8/31/16
61		0%	Sprint 39	2 wks	60	Wed 9/14/16
62		0%	<b>Milestone - Technical Development Complete</b>	0 days	2	Wed 8/3/16
63		0%	<b>Milestone: S13-500 MOD4 LexEVS Lucene Project Roadmap Complete</b>	0 days	1	Wed 9/28/16

S13-500 MOD4 LexEVS Lucene Project Roadmap

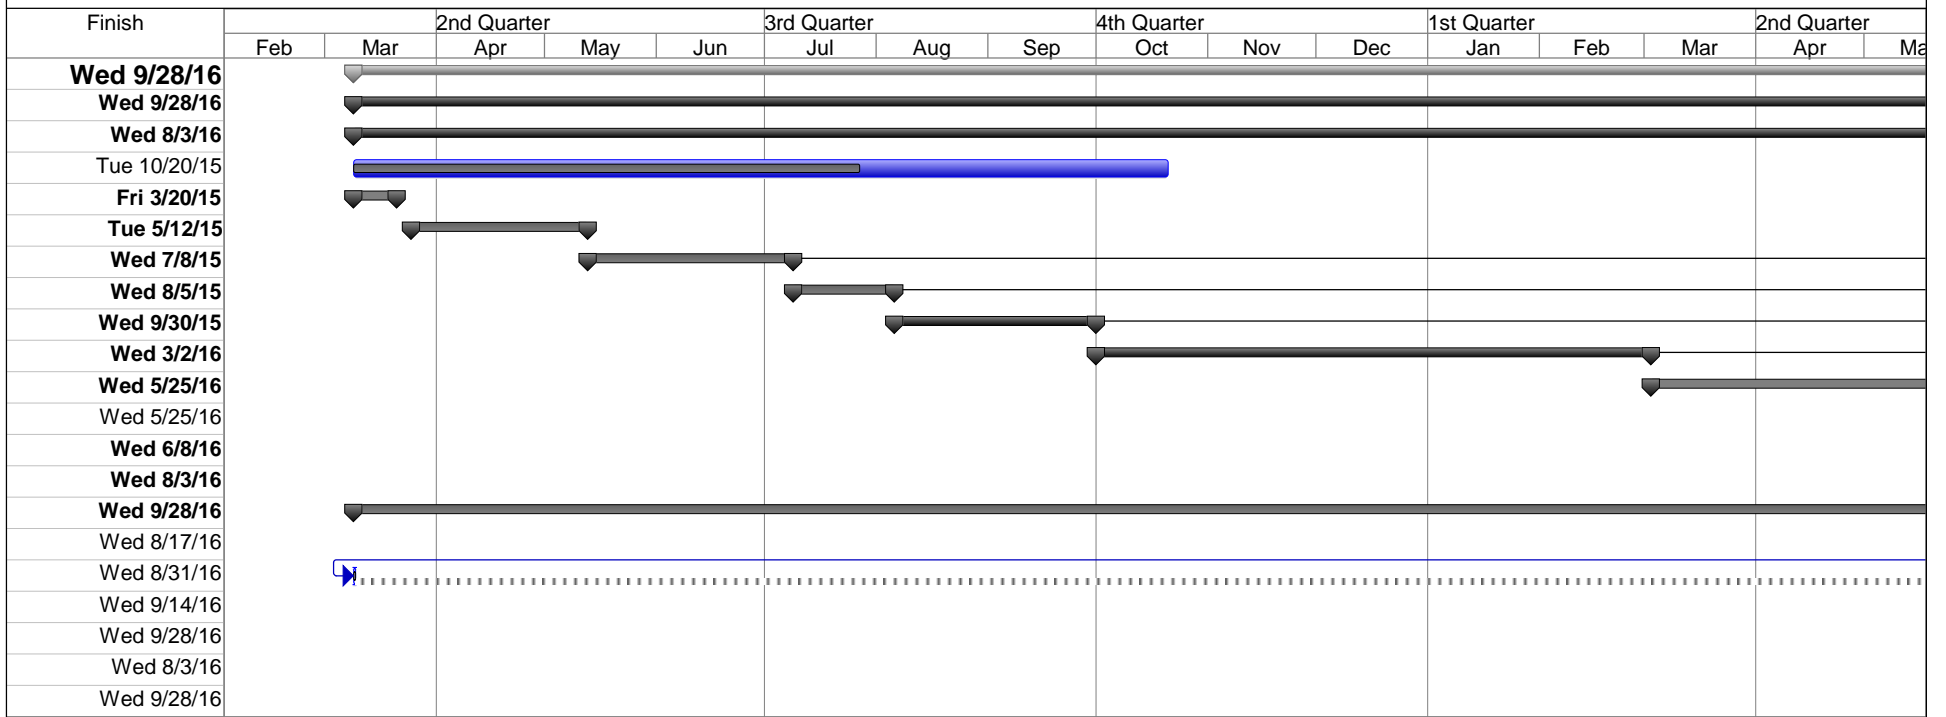

S13-500 MOD4 LexEVS Lucene Project Roadmap

